


# सिद्धार्थनगर नगरपालिका कार्यालय

सिद्धार्थनगर, रुपन्देही



आ.ब. ०७१०७२ को बार्षिक प्रगति

# सिद्धार्थनगर नगरपालिका

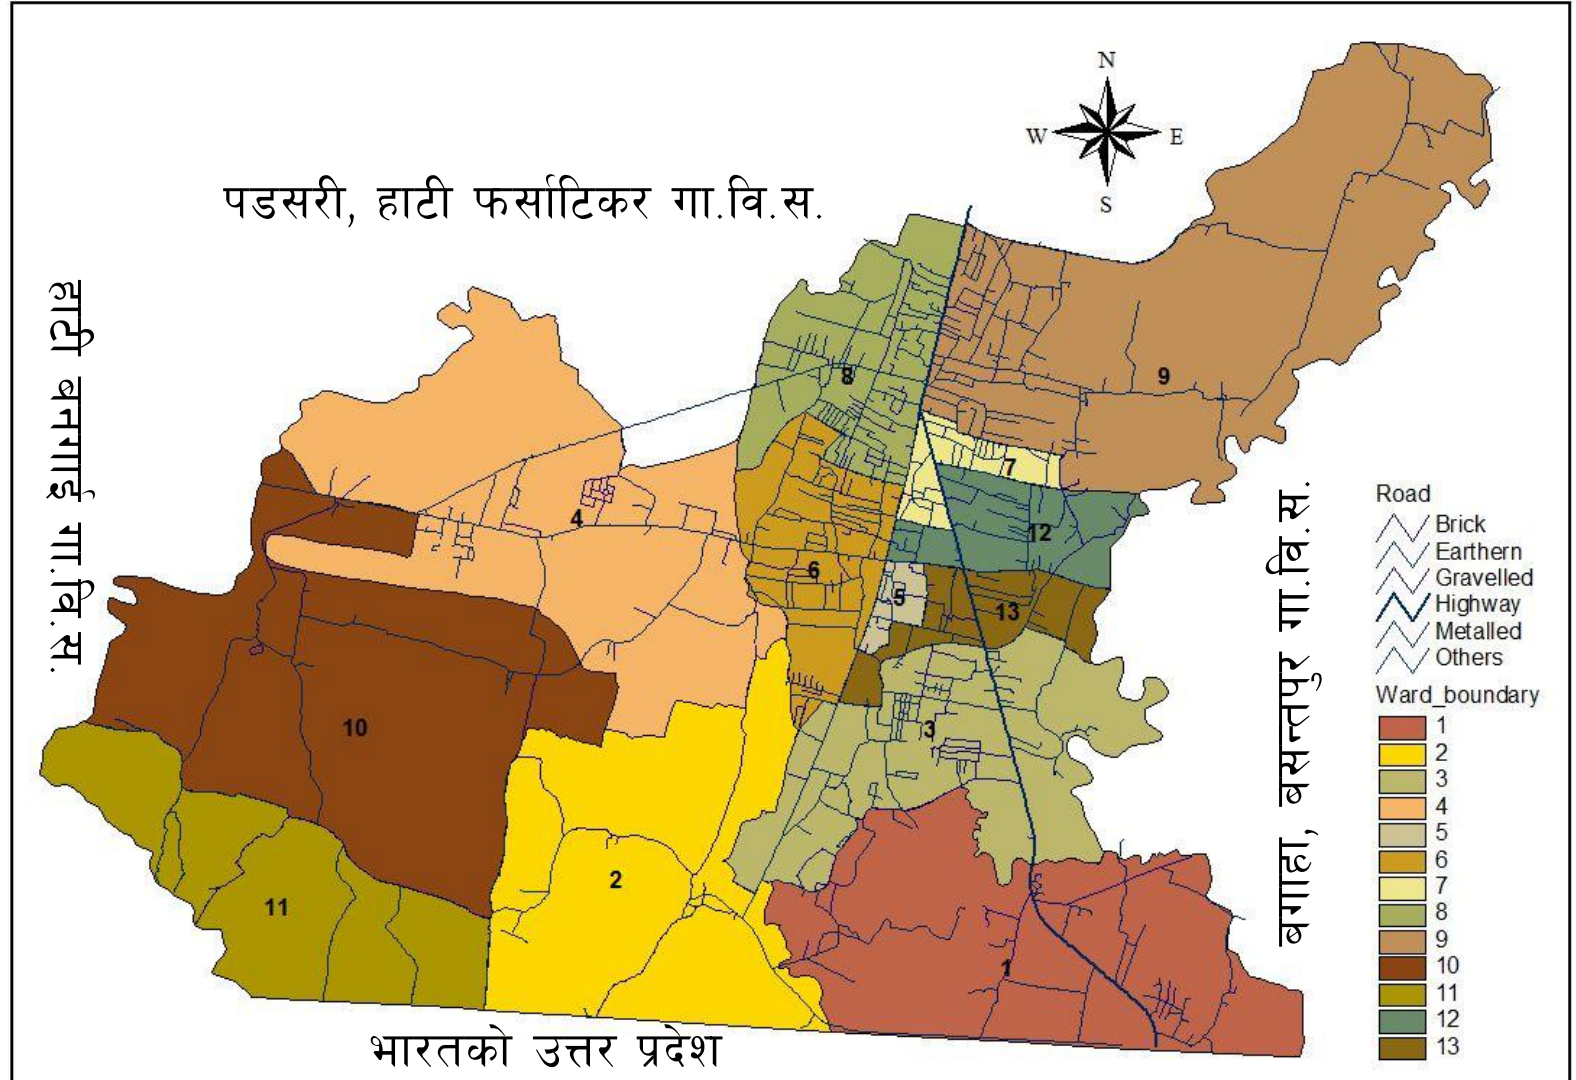

- प्रवेशद्वार
- व्यापारिक केन्द्र
- औद्योगिक केन्द्र
- पर्यटकीय केन्द्र

# हाम्रो नारा

पर्यटन, उद्योग, व्यवसाय र शिक्षा  
हराभरा बुद्धभूमि सिद्धार्थनगरको इच्छा

एक घर एक चर्पी, नजिकैमा धारा,  
खुला दिशा मुक्त नगर बनाऔं, हामी मिली सारा

# क्षेत्रफल

आवास	: ३५८ हेक्टर
कृषि योग्य	: २,९१५ हेक्टर
बजार	: ६० हेक्टर
अन्य	: २७० हेक्टर
जम्मा	: ३,६०३ हेक्टर

# हावापानी

अधिकतम तापक्रम	: ४२.२° बैशाख, जेष्ठ
न्यूनतम तापक्रम	: २° पुस, माघ
औसत वर्षा	: १४३६.५ मि. मि.

# जनसंख्या (२०६८ को जनगणना अनुसार)

पुरुष : ३१,६७३

महिला : ३१,८१०

जम्मा : ६३,४८३

(२०७२ को प्रक्षेपण ७०,०००)

वडा संख्या : १३

# सडक तथा ढलको अवस्था

- सडक पिच : ६० कि.मि. (राजमार्ग ११ कि.मि.)
- ग्रेभल : ९५ कि.मि.
- मुख्य ढल : १८.७ कि.मि.
- सहायक ढल : ३७ कि.मि.
- नामाकरण भएको सडक संख्या : ५५ वटा
- नामाकरण नभएको सडक संख्या : २९ वटा

# शिक्षा

क्र.सं.	शैक्षिक संस्था	सामुदायिक विद्यालय	संस्थागत विद्यालय	जम्मा
१.	प्राथमिक	६	५	११
२.	निम्न माध्यामिक	३	२	५
३.	माध्यामिक	६	१६	२२
४.	उच्च माध्यामिक	२	४	६
५.	मदरसा	१०		१०
६.	क्याम्पस (कलेज)	४	६	१०

# स्वास्थ्य

भीम अस्पताल (जिल्ला अस्पताल)	: १
लुम्बिनी रण-अम्बिका आँखा अस्पताल	: १
युनिभर्सल मेडिकल कलेज शिक्षण अस्पताल	: १
श्रीकृष्ण नेत्रालय	: १
लुम्बिनी नेत्रालय	: १
मर्चवार पोलिक्लिनिक प्रा.लि.	: १
भैरहवा हस्पिटल प्रा.लि.	: १
सिद्धार्थनगर सीटी हस्पिटल प्रा.लि.	: १
नगर स्वास्थ्य केन्द्र	: २



# नगरपालिकाको जग्गा

नगरपालिकाको स्वामित्वमा रहेको जग्गा :

१०२-७-१३.५८ विगाहा

(कार्यालय, बसपार्क, सिद्धार्थ बाल उद्यान, धर्मशाला, हाटबजार, पंचवाटिका, पुस्तकालय, सभागृह, सेनेटरी ल्याण्डफिल साईटको जग्गा समेत)

## कर्मचारी दरबन्दी

◆ कुल कर्मचारी दरबन्दी	:	१४५
◆ स्थायी कर्मचारी	:	१३८
◆ करार	:	७
◆ रिक्त	:	—

आ.ब. ०७०।०७१ को MCPM नतिजाको कार्य सम्पादनमा  
८४ अंक प्राप्त गरी छैठौं स्थान प्राप्त, १५ प्रतिशत अनुदान थप

# सार्वजनिक पुस्तकालय

- पुस्तक संख्या : ६०००
- पत्रपत्रिका प्राप्त संख्या :
  - दैनिक : २१
  - साप्ताहिक : ३६
- समय : दिउँसो १ देखि साँझ ७ बजेसम्म (सोमवार बन्द)
- औसत दैनिक पाठक संख्या : १०० जना



# नगरपालिकाका कर्मचारीहरूले प्राप्त गरेका प्रशिक्षण सम्बन्धि विवरणहरू:

कम्प्युटर तालिम	:	१० जना
एकीकृत सम्पत्ति कर	:	२५ जना
कार्यालय व्यवस्थापन संचालन तालिम	:	२३ जना
शहरी विकास तालिम	:	१ जना
फोहोरमैला व्यवस्थापन तालिम	:	३ जना
<b>GIS</b> तालिम	:	६ जना
सार्वजनिक खरीद तालिम	:	४ जना
सूचनाको हक	:	४५ जना
<b>National Building Code</b>	:	१२ जना
ऋणयोजना निर्माण व्यवस्थापन तालिम	:	४० जना

# नगरपालिकाले प्रदान गरेका सिफारिस

नाता प्रमाणित	: ७९६ वटा	मृत्यु सिफारिस	: ३ वटा
दुई नाम, थर	: २३४ वटा	मुआब्जा	: ७ वटा
पेन्सन, रहलपहल	: ३६ वटा	अन्य सिफारिस	: २९५ वटा
विवाह प्रमाणित	: ५३ वटा		
जन्म प्रमाणित	: १५७ वटा	चारकिल्ला	: ७,१३१ वटा
बसोबास प्रमाणित	: २१ वटा	घरेलु उद्योग	: ५३ वटा
अविवाहित	: ५१ वटा	जग्गा नामसारी	: ३३ वटा
नाबालक	: ५७ वटा		

# नक्सा पास

नक्सा दर्ता : ५९१ वटा      अस्थायी पास : ३७८ वटा  
स्थायी पास : ४९५ वटा      निर्माण सम्पन्न : २४८

## सडक बत्ति सम्बन्धि विवरण

पोल संख्या : ४,८१३ वटा  
सि.एफ.एल. चिम : २५८२ वटा  
मर्करी (२० वाट) : ८६० वटा  
साधारण चिम : ४०२ वटा  
खाली पोल : ९६८ वटा  
जम्मा खर्च रकम रु. २४,४३,७०८।००

# व्यक्तिगत घटना दर्ता

- जन्म दर्ता : पुरुष ६८६ महिला ८३० जम्मा १,५१६
- मृत्यु दर्ता : पुरुष १४५ महिला १९५ जम्मा ३४०
- विवाह दर्ता : जम्मा ६४१
- बसाई सराई दर्ता : जम्मा २५५
- सम्बन्ध विच्छेद : जम्मा ९

# वारुणयन्त्र सम्बन्धी प्रगती विवरण

वारुणयन्त्र	: ३ वटा
कर्मचारी	: २० जना
आगलागी	: न.पा. भित्र ५७ ठाउँमा, गा.वि.स. मा १९ ठाउँमा
नोक्सानी	: रु. २,५६,७५,०००।-
न.पा.	: रु. १,१५,३०,०००।-
गा.वि.स.	: रु. १,४१,४५,०००।-
सेवा पुगेको क्षेत्र	: रुपन्देही, नवलपरासी, कपिलवस्तु भारत महाराजगंज, सुनौली
कुल खर्च	: ८३,४५,६२९।४१

# सामुदायिक मेलमिलाप केन्द्र

- जम्मा दर्ता भएको : ८१
- छलफल भएको : ५९
- सहमती भएको : ४४
- असहमती भएको : १५
- छलफल नभएको : २२



# सामाजिक सुरक्षा भत्ता वितरण विवरण

विवरण	ज्येष्ठ नागरिक	दलित ज्येष्ठ नागरिक	एकल महिला र विधवा	पूर्ण अपांग	आंशिक अपांग	अति असक्त अपांग	दलित बालबालिका	लोपोन्मुख
महिला	७३१	९१	११३१	८	३	४	१०	११
पुरुष	५४४	११९		९	७	६	८	१२
जम्मा	१२७५	२१०	११३१	१७	१०	१०	१८	२३
भुक्तानी	७५,४२,०००.००		६७,३२,०००.००	१६८,८००.००			२५,६००.००	२७६,०००.००
उपचार खर्च	२३,००,०००.००							
कुल जम्मा	१,७०,४४,४००.००							

# सामाजिक विकास शाखाबाट सम्पादित कार्यक्रमहरु:

१. वृहत नगर स्तरिय पांचदिने सरसफाई अभियान ।
२. वृहत नगर स्तरिय सरसफाई कार्यक्रममा नेपाल सरकारको मुख्य सचिव श्रीमान् लिलामणी पौडेल ज्यूको आतिथ्यमा समिक्षा कार्यक्रम ।
३. वडा नं.१ देखि १३ वडामा वडा स्तरिय सरसफाई विषयक १/१ दिने छलफल कार्यक्रम ।



# सामाजिक विकास शाखाबाट सम्पादन भएका कामहरु:

४. १३ वटै वडामा वडा स्तरिय वृहत सरसफाई समितिको गठन ।
५. १ देखि १३ वटै वडामा वृहत वडा स्तरिय सरसफाई समितिको सकृयतामा सरसफाई कार्यक्रम भई रहेको ।



# सामाजिक विकास शाखाबाट सम्पादन भएका कामहरु:

## जनचेतनामुलक कार्यक्रम :

१. सि.न.पा.को आर्थिक सहयोगमा दरखसवा महिला समुह वडा नं.३ द्वारा ६० जनालाई फोहोरमैला व्यवस्थापन 3R दण्ड जरिवाना EFLG, CFLG विषयक २ दिने तालिम कार्यक्रम ।
२. सि.न.पा.को सहयोगमा सिद्धार्थ सामुदायिक सेवा केन्द्र ५,१२ र १३ द्वारा ७० जनालाई घरेलु हिंसा विषयक १ दिने गोष्ठी ।
३. सि.न.पा. को सहयोगमा बौद्धिक अपाङ्गता अभिभावक संघ द्वारा ५० जनालाई सचेतना कार्यक्रम ।



# सामाजिक विकास शाखाबाट सम्पादन भएका कामहरु:

## बालबालिका सम्बन्धी कार्यक्रम :

१. सि.न.पा. द्वारा LGCDP को कार्यक्रम अन्तरगत नि.मा.वि.र मा.वि.मा अध्ययनरत करिब ६० जना विद्यार्थीहरुका लागि एकदिने बालमैत्री स्थानीय शासन बिषयक अभिमुखीकरण कार्यक्रम ।



# सामाजिक विकास शाखाबाट सम्पादन भएका कामहरु:

## खुला दिशामुक्त कार्यक्रम :

१. सि.न.पा. मा १३ वडाहरुमा १२०२५ घर संख्या रहेकोमा चर्पि बन्न बांकी घर संख्या २११९
२. वडा नं. ७ गत आ.ब. २०७०।७१ मा ODF घोषणा भई सकेको ।
३. यस आ.ब. २०७१।०७२ मा वडा नं.९,१२ र ५ (३) वटा वडाहरु ODF घोषणा गर्न सफल ।
४. सि.न.पा.मा जम्मा ९०३ घरमा चर्पि बन्न बांकी रहेको देखिन्छ ।
५. केही वडाहरु ODF घोषणा गर्ने तैयारीमा रहेका छन् ।



# आ.ब. ०७१०७२ को आर्थिक स्थिती

श्रोतहरु	अनुमानित आय रकम	यथार्थ आय रकम
(क) कुल बजेट	३५,५८,९७,०७४	३४,०८,८१,२४७
(अ) निसर्त अनुदान	३,२४,९२,०००	३,२४,९२,०००
(आ) शसर्त अनुदान	४,२४,२५,१४०	४,२७,४२,०७५
(इ) शसर्त अनुदान एकिकृत शहरी विकास प.	१८,००,००,०००	१४,६२,४४,९७३
(ई) राजस्व बाँडफाँड	५५,००,०००	६६,९३,३५१
(उ) आन्तरिक आय	४,८८,४८,०६१	४,७६,००,०००
(ऊ) अन्य (९२.२६%)	४,६६,३१,८७३	५,११,६७,८३४

# आ.ब. ०७१०७२ को आर्थिक स्थिती


रकम रु. हजारमा

श्रोतहरु	अनुमानित व्यय रकम	यथार्थ व्यय रकम
(ख) कुल खर्च	३५,५८,९७,०७४	३४,०८,८१,२४७
(अ) निसर्त अनुदान	३,२४,९२,०००	३,२४,९२,०००
(आ) शसर्त अनुदान	४,२४,२५,१४०	४,२७,४२,०७५
(इ) शसर्त अनुदान एकिकृत शहरी विकास प.	१८,००,००,०००	१४,६२,४४,९७३
(ई) राजस्व बाँडफाँड	५५,००,०००	६६,९३,३५१
(उ) आन्तरिक आय	४,८८,४८,०६१	४,९८,१९,९९०
(ऊ) अन्य	४,६६,३१,८७३	६,२८,८८,८५६
(ग) खर्च प्रतिशत (%)		९२.२६ %



श्रोतहरु	अनुमानित रकम	यथार्थ रकम
वार्षिक बजेट	३५,५८,९७,०७४	३३,४९,४०,२३४
(१) पूँजीगत	२६,१४,१२,०७४	२४,१२,३२,९०३
(२) चालु	९,४४,८५,०००	९,३७,०७,३३१
<b>जम्मा :</b>		
<b>(घ) निकास</b>		
(१) पूँजीगत	२,६१४,१२,०७४	२४,१२,३२,९०३
(२) चालु	९,४४,८५,०००	९,३७,०७,३३१
<b>(ङ) खर्च</b>		
(१) पूँजीगत	२६१,४१,२२,०७४	२४,१२,३२,९०३
(२) चालु (बारुण यन्त्र र सरसफाई खर्च समेत समावेश छ)	९,४४,८५,०००	९,३७,०७,३३१
<b>जम्मा :</b>		
(च) चालु खर्चबाट प्रशासनिक खर्चमा विनियोजित रकम	७,६३,८५,०००	७,६३,८५,०००
(छ) चालु खर्चबाट प्रशासनिक खर्च रकम	७,६३,८५,०००	७,२२,५२,४५९
(ज) फ्रिज रकम रु. (बाँकी रकम स्थानीय निकाय कोष खातामा आगामी बर्षलाई जिम्मेवारी सारेको)	०	५९,४१,०१२

# सिद्धार्थनगर न.पा.को बजेट सम्बन्धि विवरण

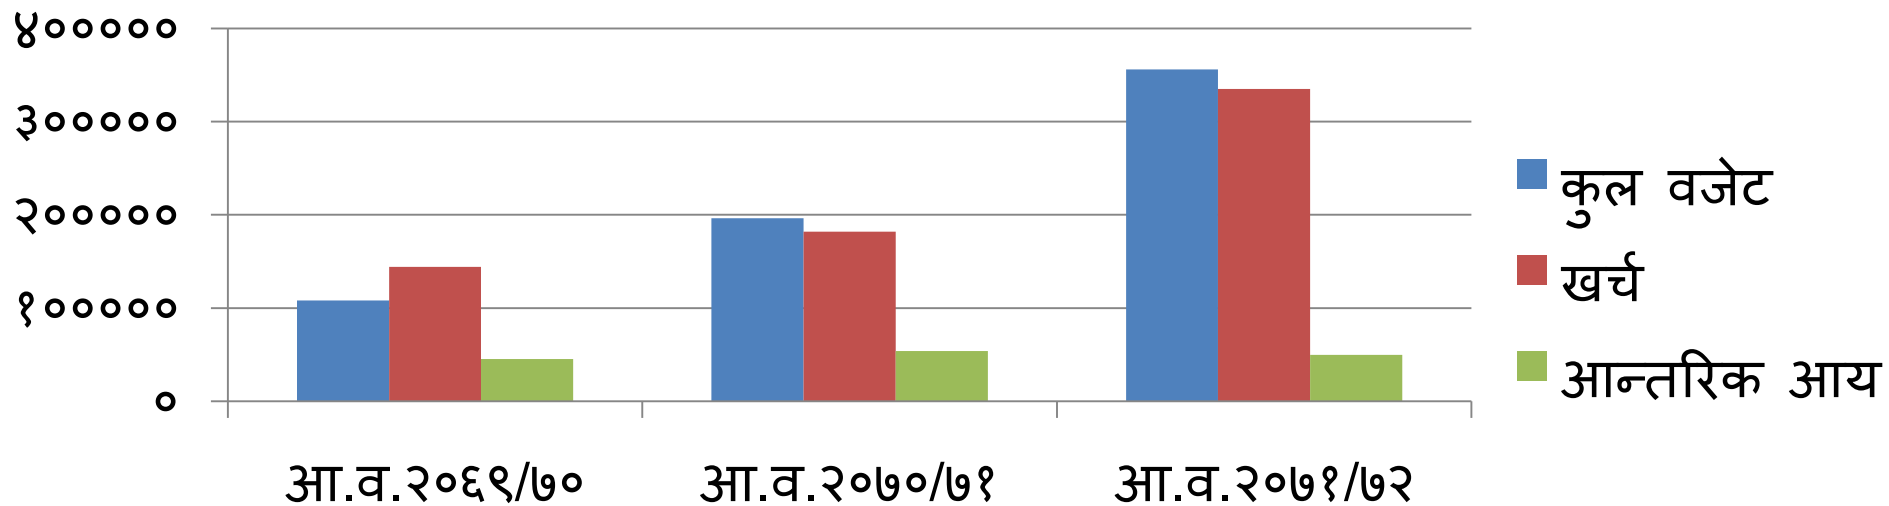

आ.ब.	अनुमानित	यथार्थ	आन्तरिक आय	आन्तरिक आय (बढी/घटी)
	कुल बजेट	खर्च		
०६९/०७०	१०८२५४५३२	१४४३००८१९	४५१८२०१४	%
०७०/०७१	१९६१९८३७५	१८१८३७८४०	५३८२७१४३	+१६.०६%
०७१/०७२	३५५८९७०७४	३३४९४०२३४	४९८१९९९०	-७.४४%

# बेरुजुको अवस्था

- १) आ.व. २०७०-७१ सम्मको कूल बेरुजु : १३५६४.००
- २) आ.व. २०६९-७० सम्मको कूल फर्छर्योट : ५२६३.००
- ३) आ.व.२०७१-७२ मा फर्छर्योट रकम : ४०८९.००  
र प्रतिशत : ४९.२७ %
- ४) आ.व. २०७०-७१ को थप बेरुजु सहित कुल बाँकी  
बेरुजु : ४२११.००
- ५) खर्चको अनुपातमा बेरुजु प्रतिशत : २.३२%

आ.व. २०७०/७१ को कुल खर्च १८,१८,३७,८४०/९८ को अनुपातमा कुल बेरुजु प्रतिशतमा राखिएको)

# भौतिक प्रगति

विवरण	इकाई	प्रगति	
		परिमाण	रकम
पक्की नाला	मी.	३२८४	१,६५,८४,१३२।४२
सडक पीच	मी.	१८५०	१,०१,०१,२८५।३०
सडक ग्रेभल	मी.	६५९१	७५,८७,०८१।६२
सहरी सडक मर्मत पीच	वर्ग मी.	१८८०७।३४	१,२२,९७,२७४।००
भवन मर्मत	वटा	१०	५१,८२,९७१।७७
अन्य - कल्भर्ट, ह्युमपाईप			४,५०,४०२।३५
जम्मा रकम :			५,२२,०३,१४७।४६

# उल्लेखनीय तथा अनुकरणीय कार्यहरु:

- अतिक्रमित सार्वजनिक जग्गालाई अतिक्रमण हटाई सो स्थानमा पार्किंग तथा शहरी सेवा केन्द्र निर्माण गरि शहरी सुन्दरता र आय वृद्धि गर्न योजना संचालन गरिएको।
- PPP अवधारणा अन्तर्गत सभागृह र पार्कको संचालन र व्यवस्थापनमा निजी क्षेत्रको संलग्नता कायम गरि न.पा.को आय वृद्धि, खर्च कटौती र भौतिक संरचना विकासको साथै शहरी सुविधामा वृद्धि।
- प्रशासनिक खर्च कटौतीका लागि रिक्त रहेका दरबन्दी खारेज (रिक्त रहेका) गर्ने नीतिगत व्यवस्था।
- फोहोर मैला व्यवस्थाका लागि बृहत नगर सरसफाई अभियान आयोजना गरि १० हजार नगर वस्तीहरुको सहभागिता।
- रु. दश लाख माथिका सबै योजनाहरु e-bidding गरी पारदर्शी योजना संचालन गरिएको।
- नदी उकासको जग्गालाई न.पा.को नाममा लागत कायम गरी सार्वजनिक हितको निमित्त (खानेपानी) उपयोग गरिएको।

# मुख्य मुख्य समस्या र समाधानका उपायहरु

सि.नं.	समस्या	समाधानका उपायहरु
1	न्यून आन्तरिक आयको कारण म्यचिंग फण्डमा कठिनाइ	आन्तरिक आय वृद्धिका लागि IPT लगाईएको नयाँ स्थानहरु पहिचान गरि कर संकलन गरिएको र म्यचिंग फण्डको लागि मन्त्रालयमा अनुरोध गरिएको
2	छाडा वस्तु (पशु)	जिल्ला ट्राफिक कार्यालयको सहयोगमा छाडा पशु नियन्त्रण गर्ने कार्य निरन्तर गर्ने गरिएको छ
3	डुबान	IUDP कार्यक्रम अन्तर्गत १३ कि.मि. नयाँ ढल निर्माण र ३८ कि.मि. मौजुदा ढल मर्मत सुधार कार्यक्रम तर्जुमा भएको
4	शहरी सडक व्यवस्थापन	IUDP कार्यक्रम अन्तर्गत ९ कि.मि. शहरी सडक निर्माण योजना तर्जुमा भएको
5	प्रशासनिक (चालु) खर्च वृद्धि	अनावश्यक दरबन्दी खारेज गरिएको
6	फोहोरमैला व्यवस्थापनमा सुधार गर्न नसकिएको	IUDP कार्यक्रम अन्तर्गत फोहोरमैला प्रशोधन केन्द्र स्थापनाका लागि ६ बिगाहा जग्गा प्राप्त गरिएको. टोल सुधार मार्फत जनचेतनामूलक कार्यक्रम संचालन

## समस्या समाधानका लागि गरिएका प्रयाशहरू :

- आन्तरिक श्रोत वृद्धिका लागि आयमुलक योजनामा लगानी वृद्धि गरिएको आ.ब. ०७१/०७२ को कूल पुँजीगत लगानी मध्ये २ करोड १० लाख आयमुलक योजनामा लगानी गरिएको।
- प्रशासनिक खर्च कटौतीका लागि अनावश्यक रहेका दरबन्दीहरू खारेजी गरिएको (आ.ब. ०७१/०७२ मा ६ वटा दरबन्दी खारेज गरिएको)।
- नगरको सरसफाई अवस्थामा सुधार गर्न बृहत सरसफाई अभियान नगरपालिका तह र वडा एवं टोल तहसम्म संचालन गरिएको।
- सार्वजनिक सम्पत्तिको संरक्षण र उपयोगमा जोड दिईएको।

जगेडा कोषवाट प्राप्त रकमवाट वडा नं. १० मा निर्माण सम्पन्न सडक पीच



सभासदवाट प्राप्त रकमवाट वडा नं. ९ मा निर्माण सम्पन्न गेट रुपन्देही कल्जमा फर्निचर





जगोडा कोषबाट प्राप्त रकमबाट वडा नं. ३  
काटागाउँमा सम्पन्न सडक पीच तथा नाला



जगोडा कोषबाट प्राप्त रकमबाट वडा नं. १२  
रुद्रपथमा सम्पन्न नाला र सडक ग्रेभल



जगोडा कोषबाट प्राप्त रकमबाट वडा नं. ७  
हिमालीपथमा सम्पन्न सडक पीच तथा नाला




TDF वाट प्राप्त रकमबाट हाटवजारमा निर्माण  
सम्पन्न पसल घर



समावेसी पथ सिनपा द मा ६० ४० रकमवाट निर्माण सम्पन्न नाला र  
वडानं. १० मा ८०२० मा निर्माण सम्पन्न ग्रेभल सडक



सडक वोर्डवाट प्राप्त रकमवाट विभिन्न स्थानमा निर्माण सम्पन्न पीच मर्मत काम

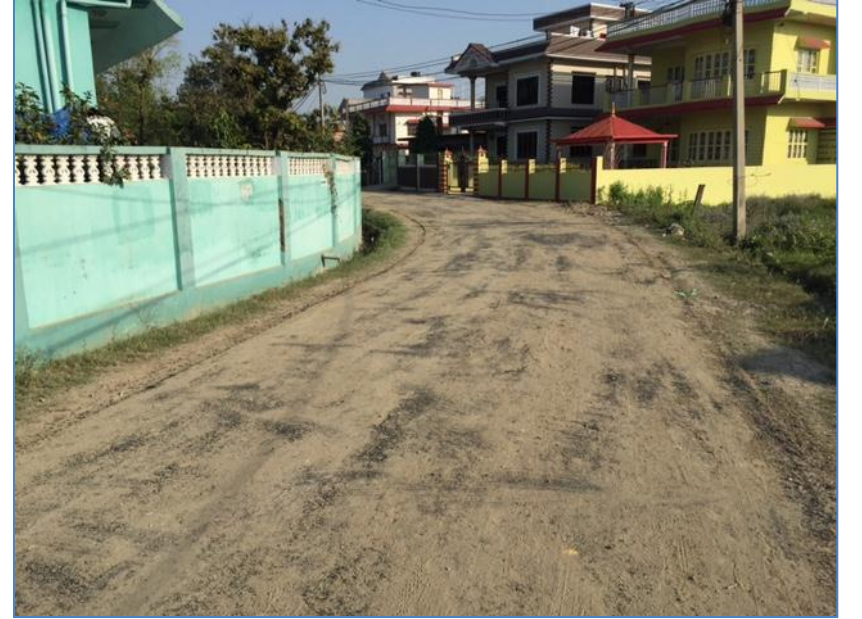

जगेडा कोषबाट प्राप्त रकमबाट वडा नं. ८  
एकता पथमा सम्पन्न सडक पीच तथा ब्लक  
सोलिंग



# एकीकृत शहरी विकास आयोजना (IUDP) तर्फको प्रगति

# एकीकृत शहरी विकास आयोजना (IUDP) को उद्देश्य

- (१) भौतिक निर्माण
  - (क) व्यवस्थित फोहोरमैला व्यवस्थापन
  - (ख) डुबान समस्या समाधान
  - (ग) सडक स्तरोन्नती
- (२) सामाजिक विकास, विपन्न वस्तीहरुको लागि
  - (क) जनचेतना अभिवृद्धि कार्यक्रम
  - (ख) क्षमता विकास मार्फत आय आर्जन कार्यक्रम
  - (ग) साना भौतिक निर्माण कार्यक्रम

# Project Cost

US\$ million

Description		Cost Estimate	Proposed
A. Investment Costs			
1. Civil Works			
a. Solid Waste Management Improvement		3.37	
b. Storm Water Drainage Improvement		6.78	
c. Road Improvement		1.77	
d. Community Infrastructure		0.32	
	<b><i>Sub Total of Civil Works :</i></b>	<b><i>12.24</i></b>	
2. Environment and Social Mitigation		0.60	
3. Consultant			
a. Design and Supervision		1.16	
b. NGO Services		0.58	
	<b><i>Sub Total of Consultant :</i></b>	<b><i>1.74</i></b>	
	<b><i>Sub Total of A (Investment Cost):</i></b>	<b><i>14.57</i></b>	
B	Recurrent Costs	0.61	
C	Contingencies	2.00	
	<b><i>Total Project Cost :</i></b>	<b><i>17.18</i></b>	

# Cost Sharing Arrangement


Component	Central government Support			Municipal contribution	
	Government contribution	ADB loan converted to grant	ADB grant provided as grant	ADB loan onlent to loan from TDF	Municipal cash contribution
Drainage, Solid Waste and Roads	25%	55%	0%	15%	5%
Community development	12%	0%	68%	0%	20%
Consultants	20%	0%	80%	0%	0%
Incremental recurrent costs	19%	0%	51%	0%	30%
Land acquisition and resettlement	80%	0%	0%	0%	20%



## Progress of Subprojects

- Total cost estimate for Improvement and Development of Storm Water Drainage and Urban Road Subproject - **NRs. 796,852,100.30** with VAT 13%. Contract Amount is **NRs. 796,775,701.88** with VAT and contractor is China Guangzhou-Sharma & Co. Pvt. Ltd, JV. Contract Agreement has been signed on **15th December 2014**. **Work commencement on 12 Feb 2015**. Project is going on.
- Total cost of ISWM Sub-Project is **NRs. 327,775,951.75** including price contingencies 5%, physical contingencies 5% and VAT 13%. Bid opening was done on 12 Dec 2014 and **technical evaluation has completed and financial bid was open on 15 April 2015**. Bid price is above than cost estimate so Rebidding process is going on.

# MAP SHOWING PROPOSED STORM WATER DRAINAGE NETWORK FOR IMPROVEMENT

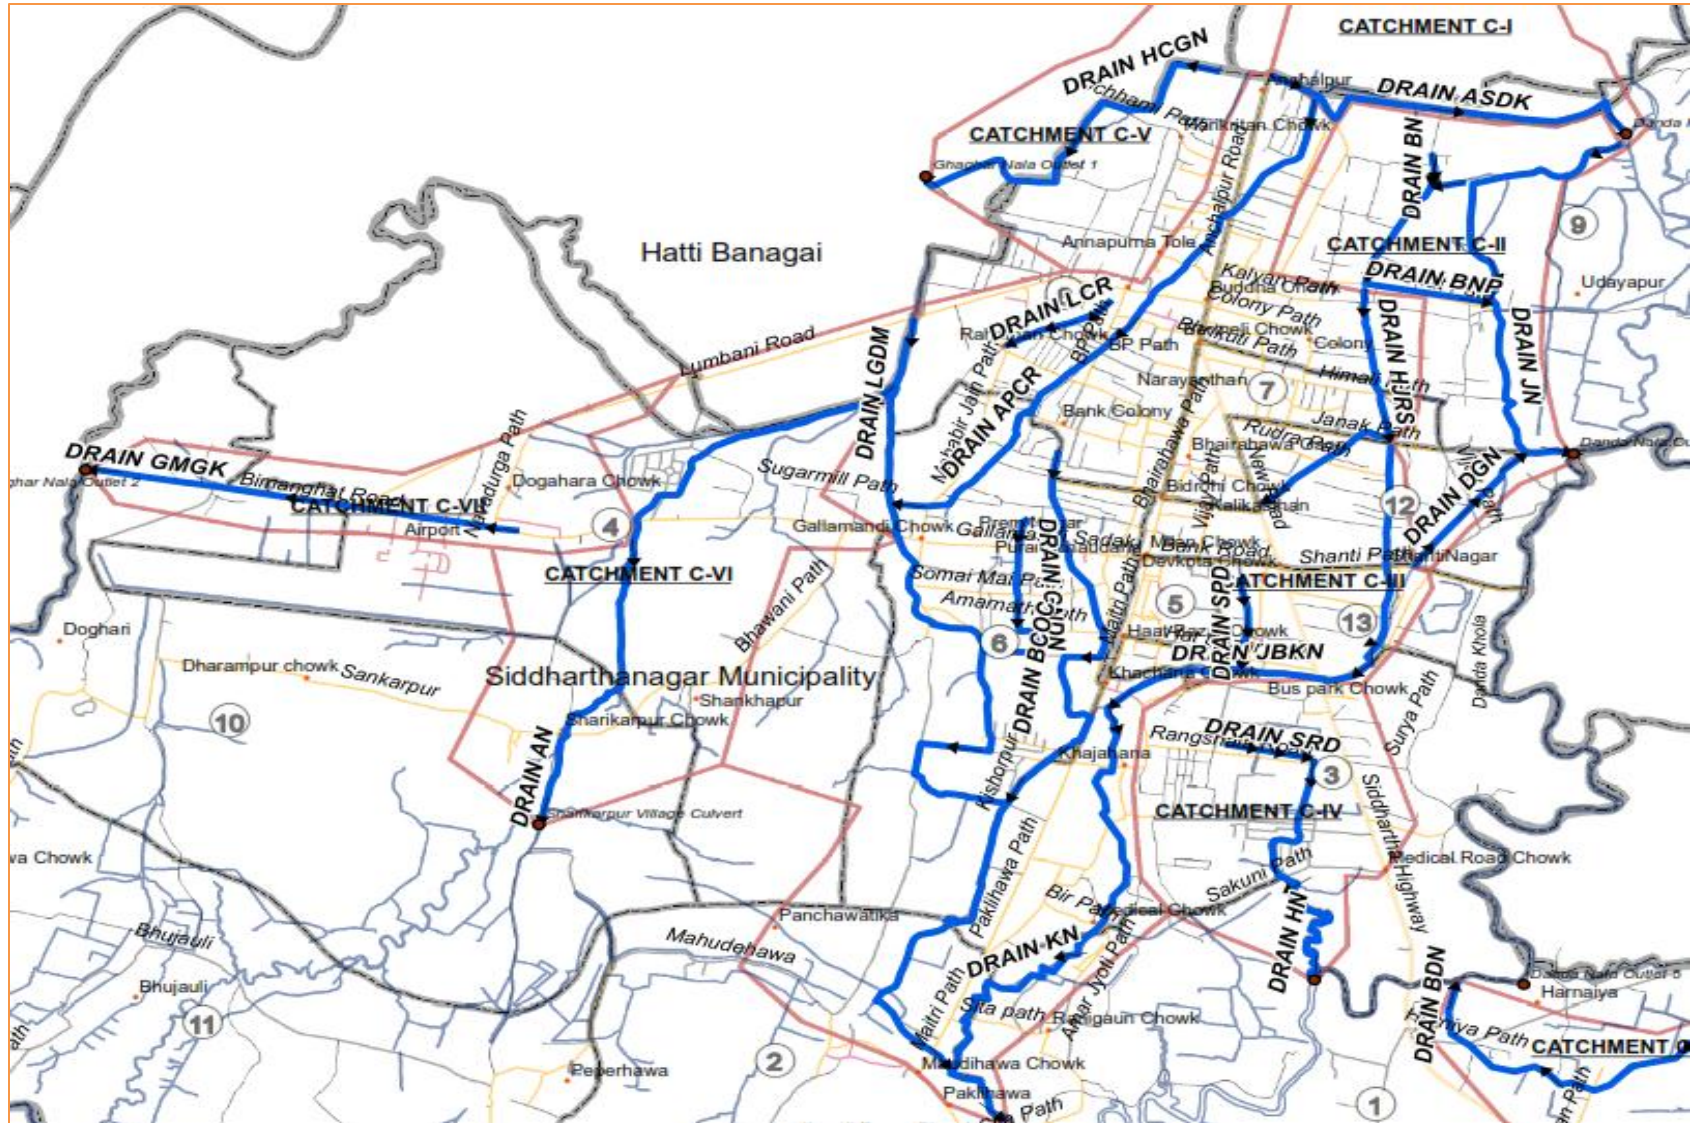

## NAME OF PROPOSED STORM WATER DRAINAGE FOR IMPROVEMENT

**Length: 32.176 km. (New Construction and Rehabilitation)**

**Length: 22 Km (Cleaning of Existing Drain) – Constructed 2390 meter**

S. N.	Drain Code	Description	Outlet Point	Length (Km)	Type of Drain	Remarks
1	ASDK-1 to 6	Anchalpur Chowk to Sano Dumdumwa Khola (Diversion Drain)	Sano Dumdumwa Khola, Outlet 1	1.769	Type-1, Trapezoidal Concrete Section	
2.1	LGDM-1 to 4	Lumbini Road to Galamandi Road to Durga Colony to Culvert at Meodihawa	Danda Nala, Outlet-4	1.718	Type-2, Rectangular Brick masonry with Trapezoidal Concrete Benching	
2.2	LGDM-5 to 10	(Paklihawa Road)		2.991	Type-5, Stone Pitching Trapezoidal Drain	
	AN-1 to 7	Lumbini Road to Galamandi Road to Culvert at Shankarpur Village	Culvert at Shankarpur	2.958	Type-5, Stone Pitching Trapezoidal Drain	Airport Nala <b>1000 m.</b>


S. N.	Drain Code	Description	Outlet Point	Length (Km)	Type of Drain	Remarks
4	APCR-1 to 6	Anchalpur to Lumbini Road to BP Path to Children's Park Road	LGDM Drain	2.806	Type-2, Rectangular Brick masonry with Trapezoidal Concrete Benching	
5	BNP-1 to 4	Brihaspati Nala to Prabhat Path to Jharan Khola	JN Drain	1.243	Type-2, Rectangular Brick masonry with Trapezoidal Concrete Benching	<b>40 m.</b>
6	BN-1	Way to Sano Dumdumwa to Near Brihaspati College	BNP	0.368	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	Road side drain <b>360 m.</b>
7	JN-1 to 8	Open field near Brihaspati College to Jharan Khola to Danda Nala	Danda Nala, Outlet-2	2.469	Type-5, Stone Pitching Trapezoidal Drain	<b>300 m.</b>

S. N.	Drain Code	Description	Outlet Point	Length (Km)	Type of Drain	Remarks
8	HJRS-1 to 5	Prabhat Path to Himali Path to Janak Path to Rudra Path to Drain at Siddhartha Highway	Drain at Siddhartha Highway	1.362	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	<b>90 m.</b>
9	SPD-1	Bank Road to Haat Bazar Path to Khajana Road Nala	JBKN	0.502	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	
10	JBKN-1 to 7	Janata Path to Shanti Path to Bus park to Khajana Road Nala (North Side) to (Ohm Colony)	KN Drain at Om Colony	1.673	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	
11	KN-1 to 7	Khajana Nala near Om Colony to Culvert at Meodihawa (Paklihawa Road)	Danda Nala, Outlet-4	2.083	Type-3, Earthen Trapezoidal Drain	.
12.1	HN-1 to 2	Near Siddhartha Highway (Rangasala) to Danda Nala	Danda Nala, Outlet-3	0.668	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	Hospital Nala
12.1	HN-3			0.708	Type-3, Earthen Trapezoidal Drain	

S. N.	Drain Code	Description	Outlet Point	Length (Km)	Type of Drain	Remarks
13	GNDN-1 to 3	Behind Galamandi Road to way to Durga Colony	LGDM Drain	0.792	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	Galamandi Nala
14.1	BCOC-1E	Bank Colony to Galamandi Road to Karna Path to Om Colony	LGDM Drain	0.511	Type-4, Rectangular Brick masonry with Semi Circular Concrete Benching	From Bank Colony Path-along BP path- Ends near Gallamandi
14.2	BCOC-1W			0.513	Type-4, Rectangular Brick masonry with Semi Circular Concrete Benching	From Bank Colony Path-along BP path- Ends near Gallamandi
14.3	BCOC-1 to 6			1.842	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	

S. N.	Drain Code	Description	Outlet Point	Length (Km)	Type of Drain	Remarks
15.1	HCGN-1	Harikirtan Chowk to Culvert at Basdilwa	Ghagara Nala, Outlet-1	0.396	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	From Harikirtan Chowk- Culvert at Basdilwa <b>200 m.</b>
15.2	HCGN- 2			0.529	Type-5, Stone Pitching Trapezoidal Drain	
16	GMGK-1 to 2	Maya Devi Chowk to Ghagara Nala	Ghagara Nala, Outlet-2	1.002	Type-3, Earthen Trapezoidal Drain	
17.1	SRD-1N	Stadium Road Drain	HN Nala	0.270	Type-4, Rectangular Brick masonry with Semi Circular Concrete	Rangasala Road
17.2	SRD-1S	Stadium Road Drain	HN Nala	0.270	Type-4, Rectangular Brick masonry with Semi Circular Concrete Benching	Rangasala Road
18	DGN -1 to 2	Culvert at Shanti Path to Dadagau (Ward No. 12) to Danda Khola	Danda Nala, Outlet-2	0.815	Type-5, Stone Pitching Trapezoidal Drain	Dadagau Nala, Ward No. 12. <b>400 m.</b>
19	BDN	Dry Port area to Danda Nala	Danda Nala, Outlet-5	1.476	Type-3, Earthen Trapezoidal Drain	Belahiya Nala Ward No. 1
20	LCR	Lumbini Road to Raheman Chowk	Drain at Children's Park	0.448	Type-2, Rectangular Brick Masonry With Trapezoidal Concrete Benching	


# MAP SHOWING PROPOSED ROADS FOR IMPROVEMENT

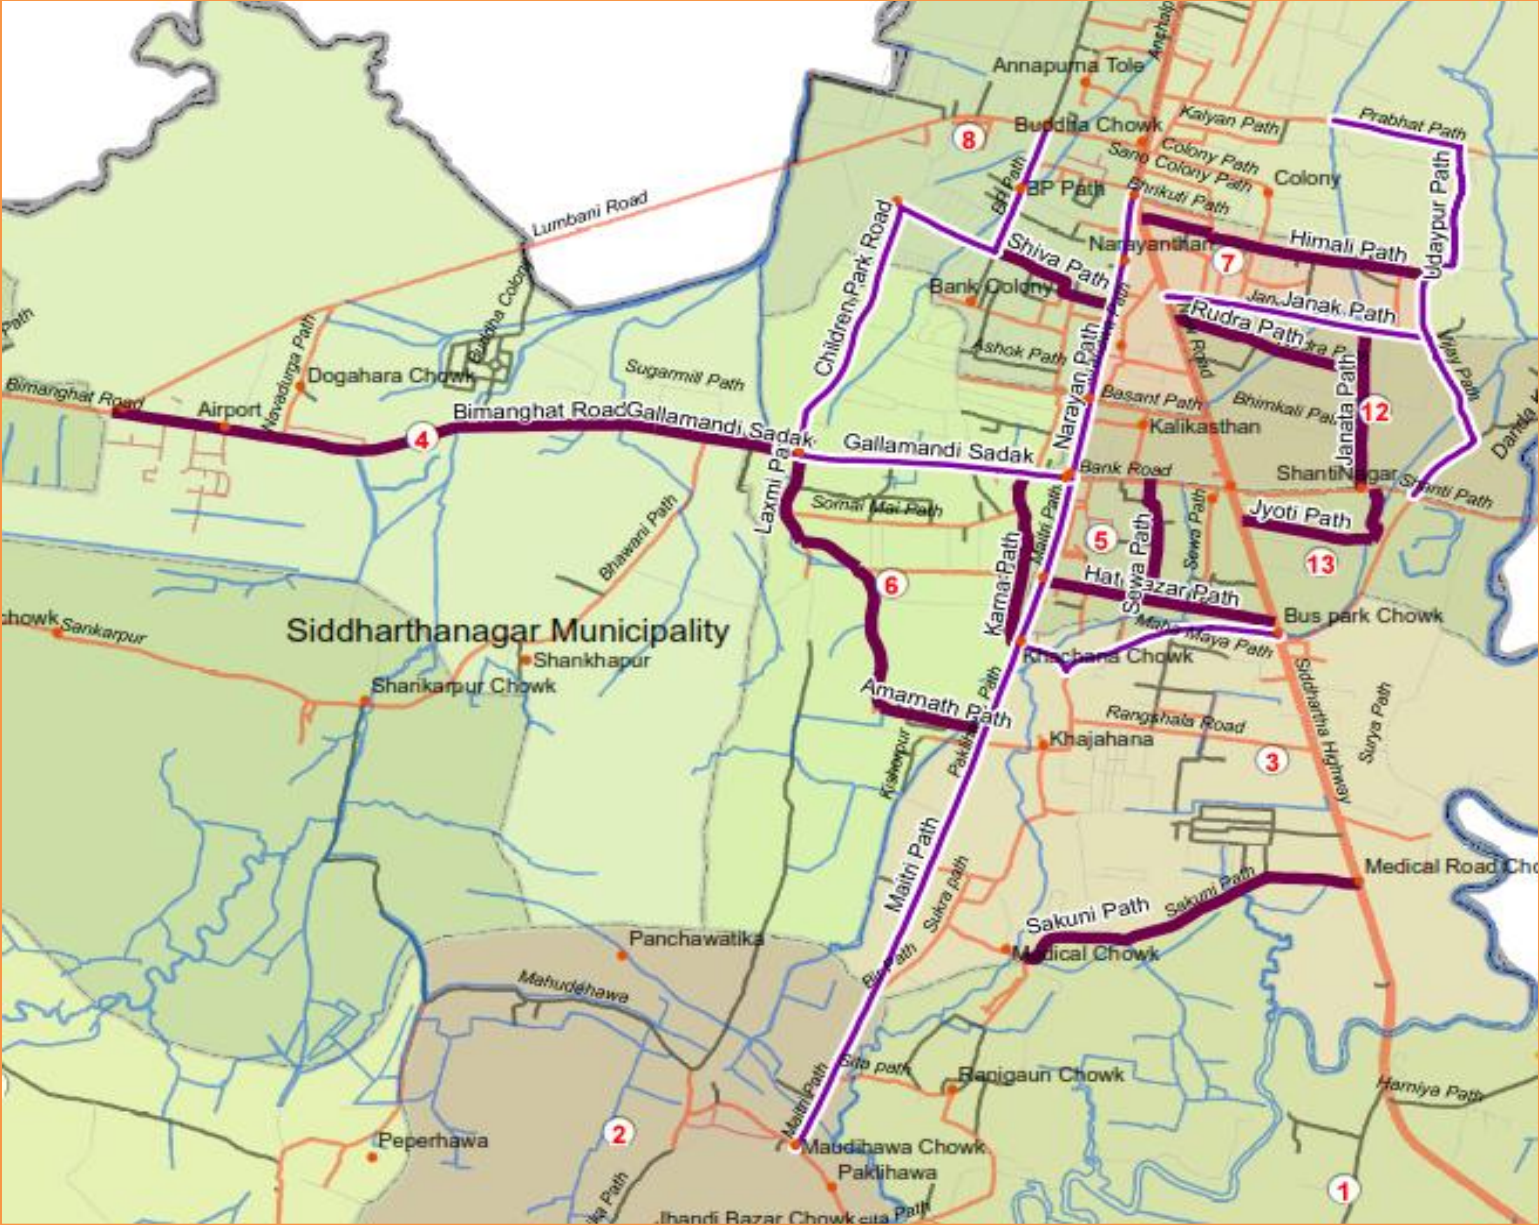





## Roads Improvement work

S. No	Road section	Design Length (m)	Designed Width (m)	Remarks
1	Maitri Path	2675.81	11	<b>Constructed Drain length = 600 m.</b>
2	Children's Park Road	1841.03	8	<b>Constructed Drain length = 300 m.</b>
3	Udayapur Road	1943.75	6	<b>Constructed Drain length= 3800 m</b>
4	Khajhana Road	920.00	5	
5	Narayan Path	1046.20	11	
6	Gallamandi	1000.00	9	
7	Janak Path	898.80	9	<b>Constructed Drain length=200 m</b>

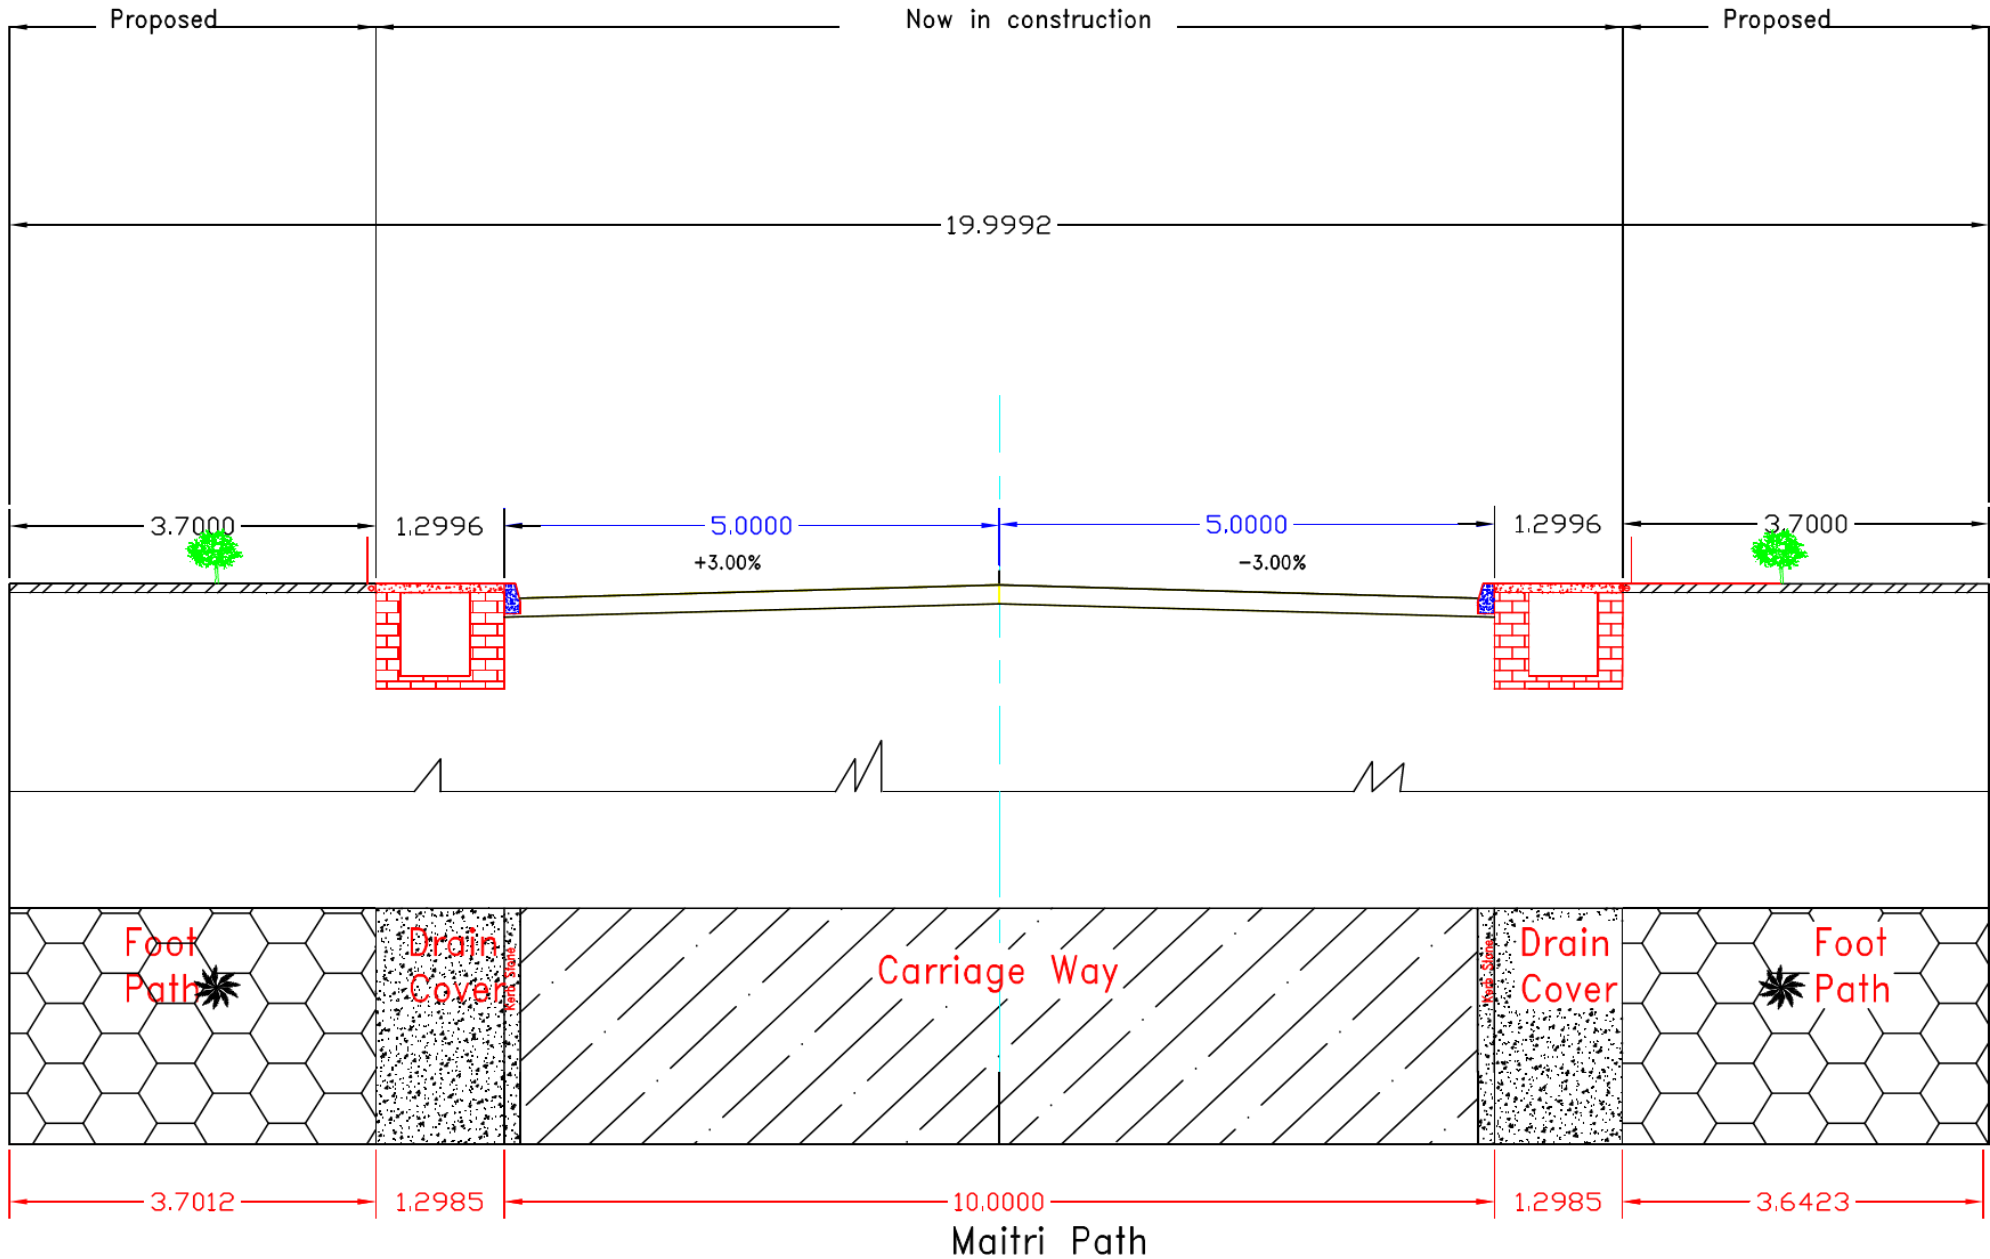


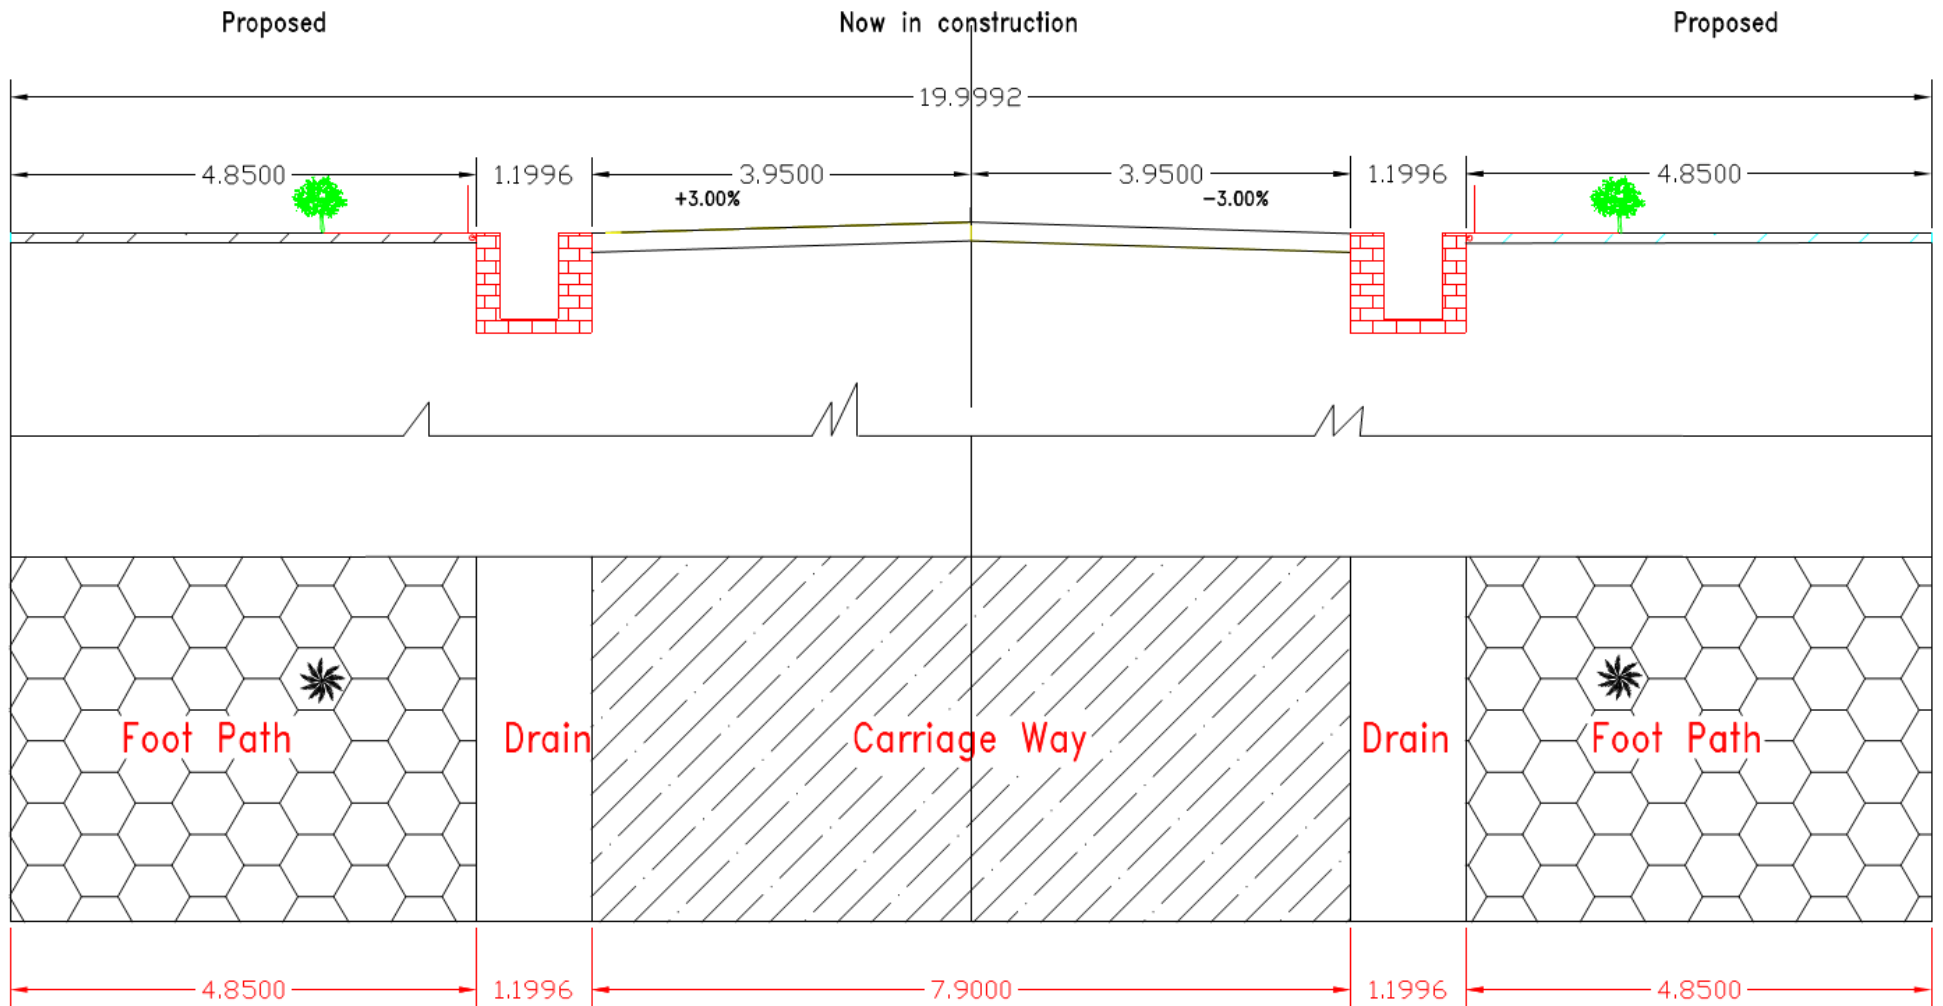


Udaypur Path (Pipal Bot to Bhairawa Baumukhi Campus)

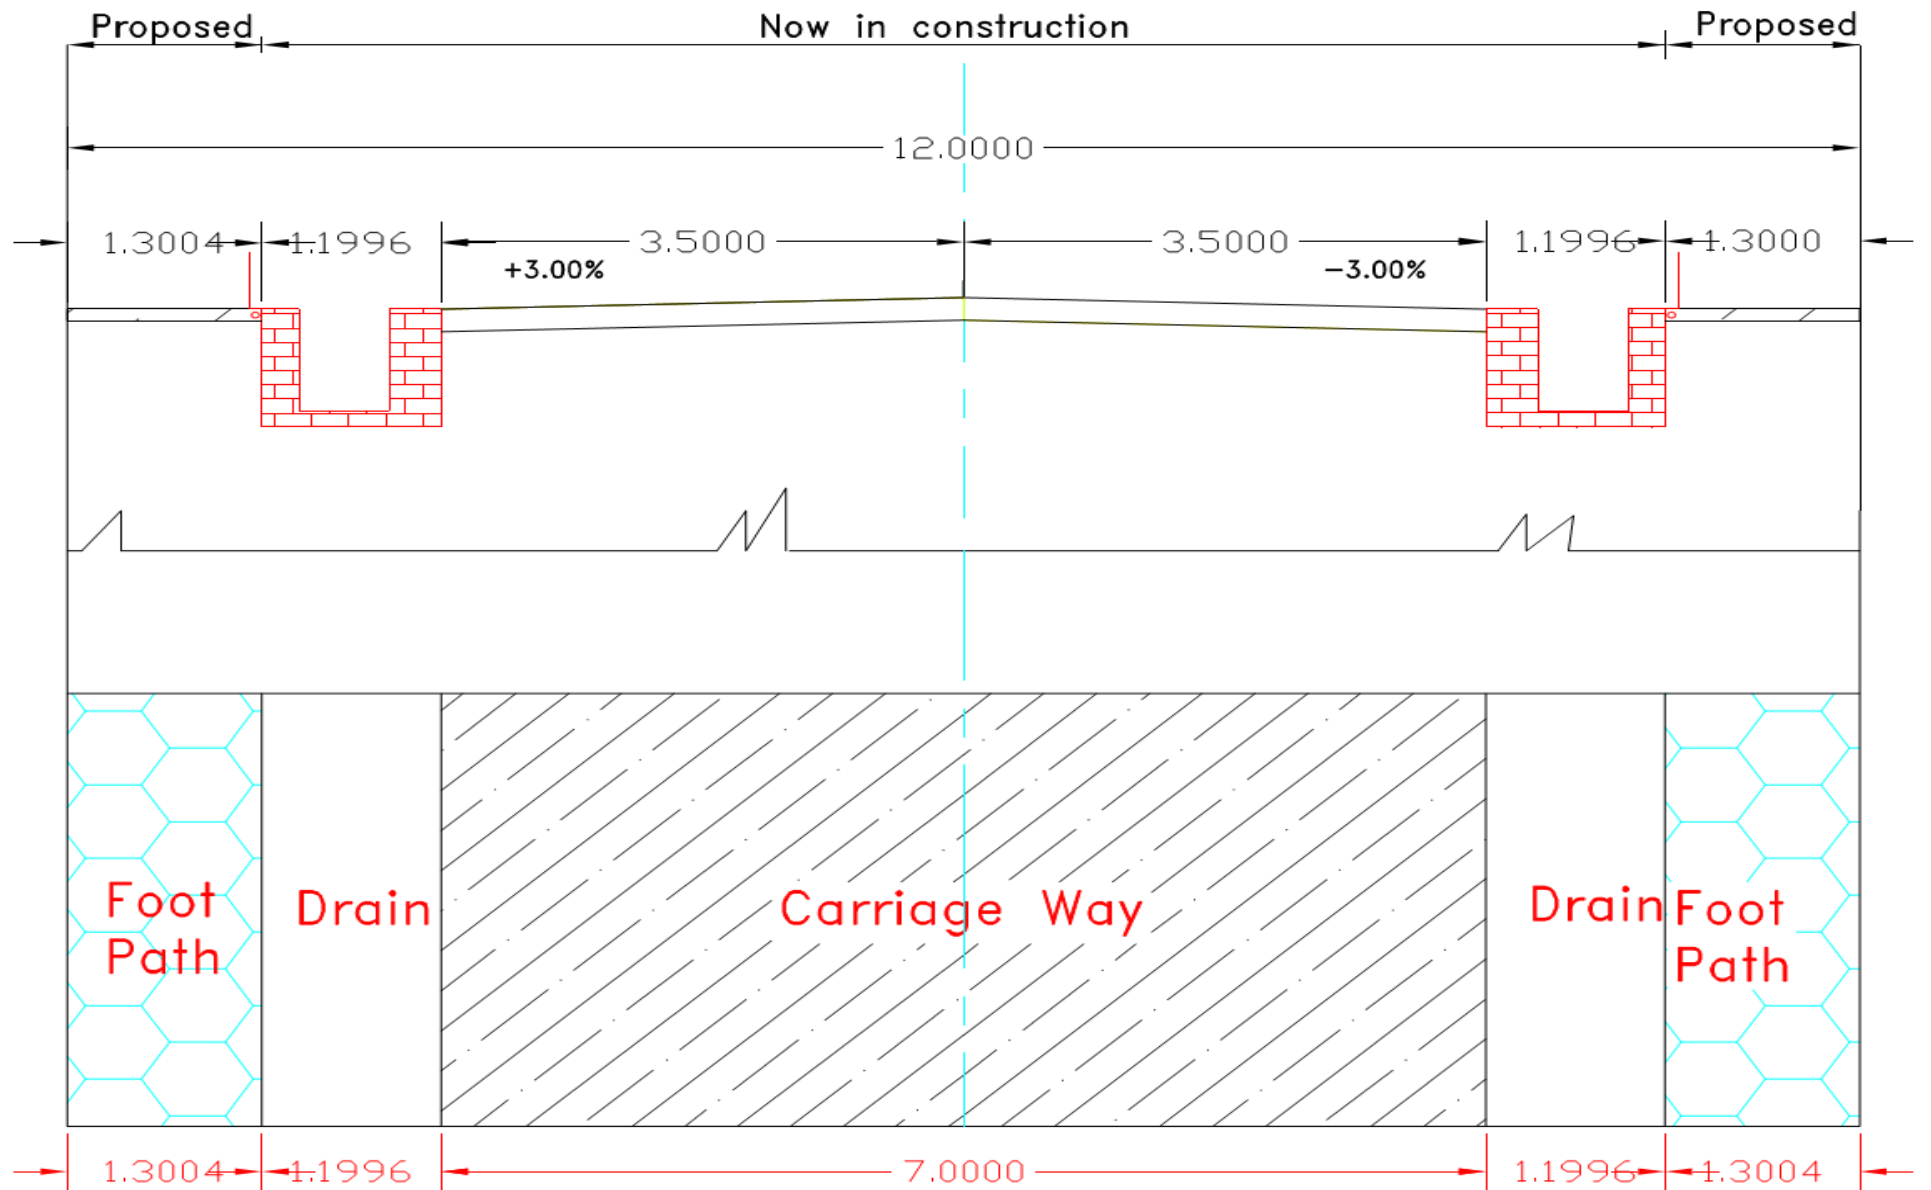



Udaypur Path (Pipal Bot to ward no 9 office)

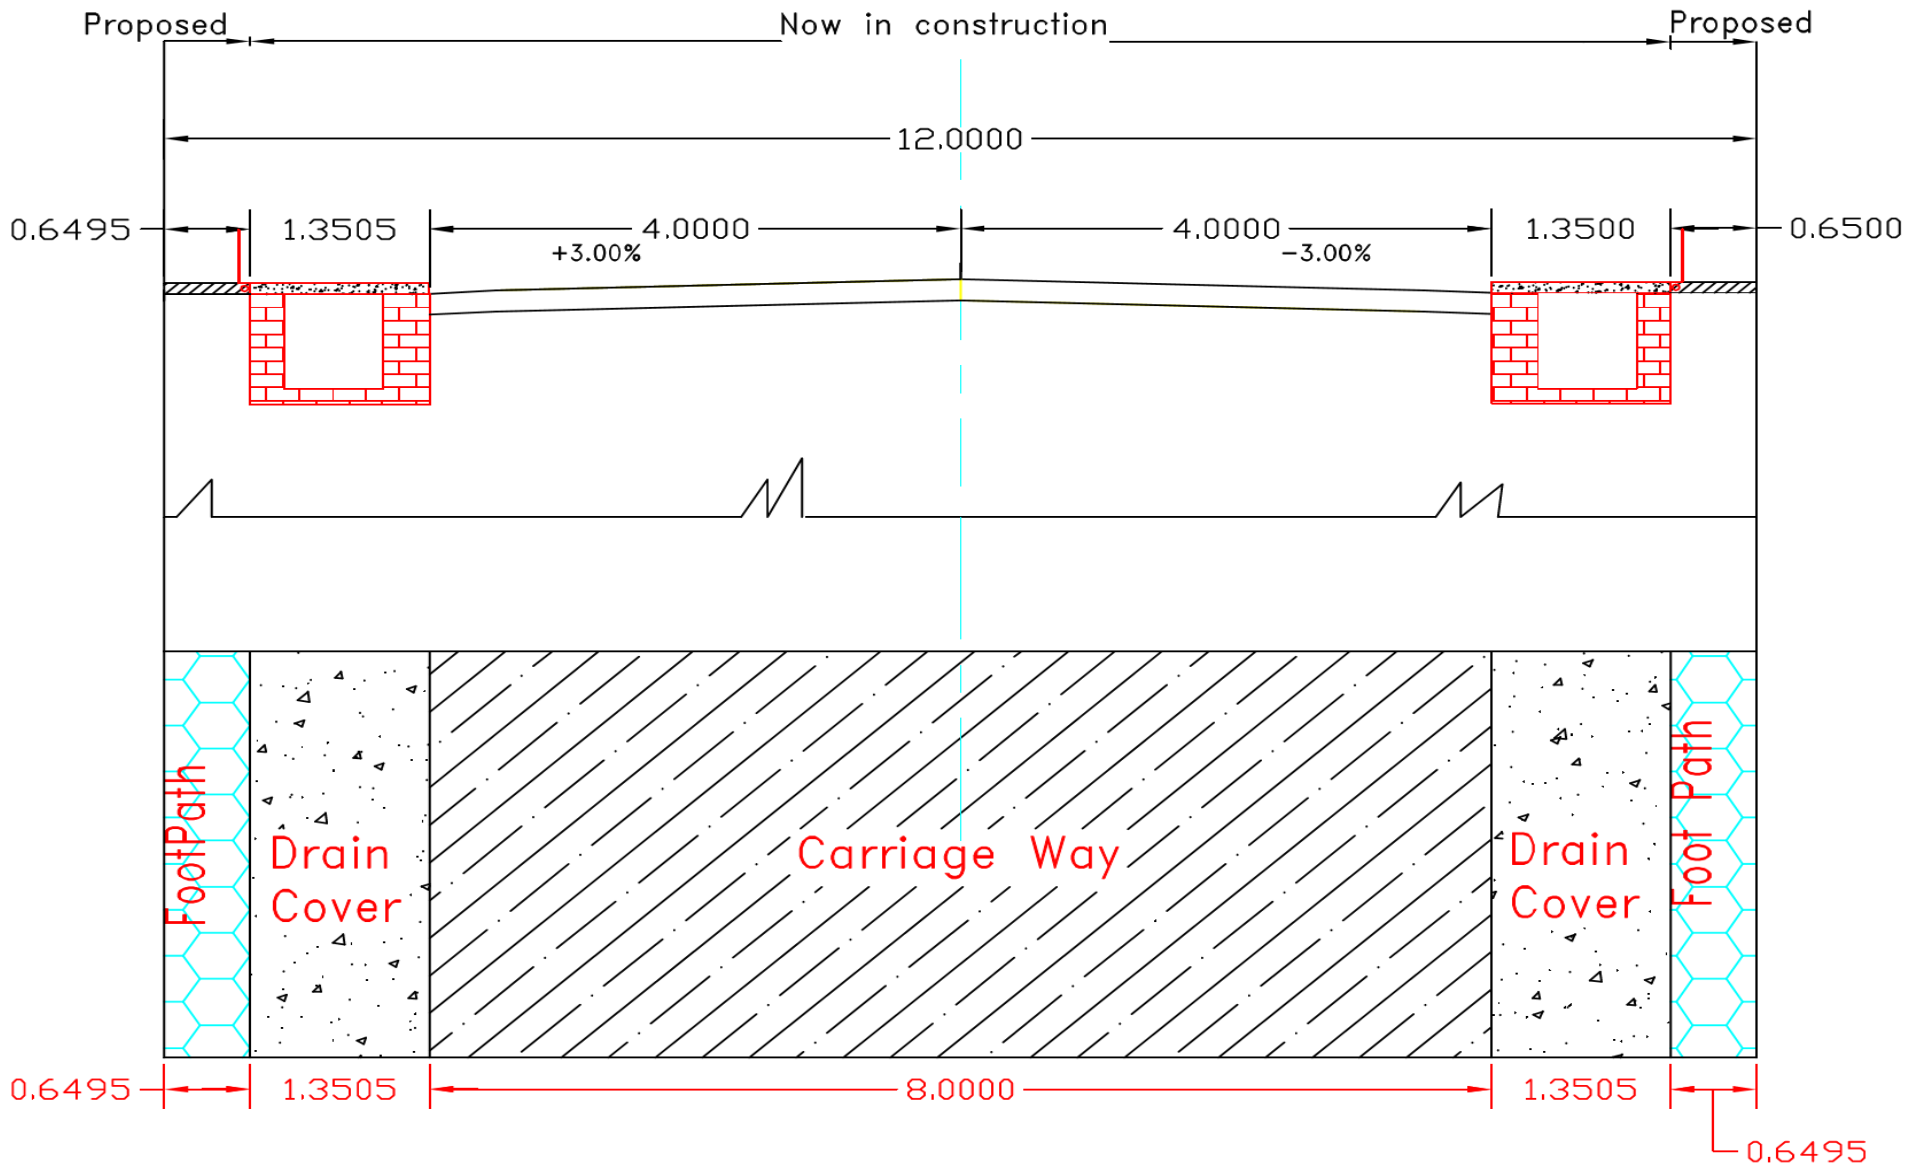


Children Park Road

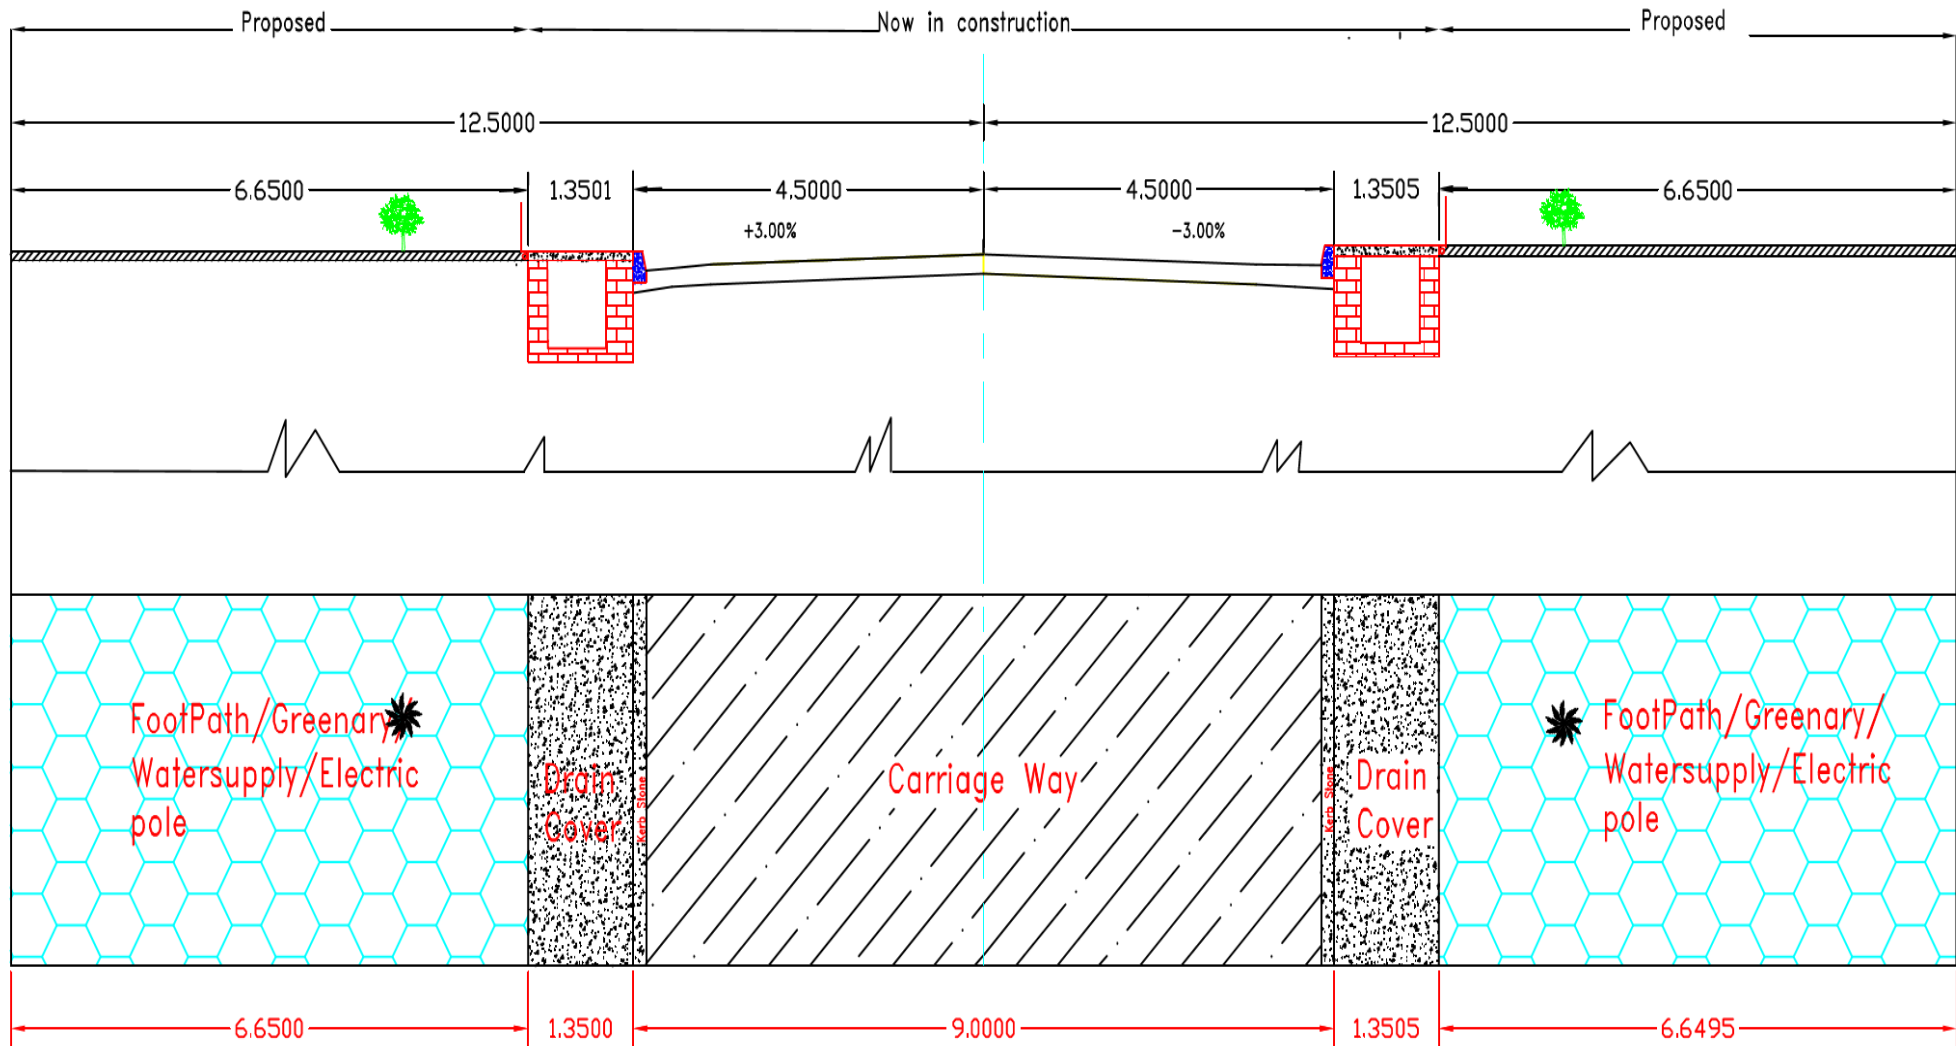

Janak Path

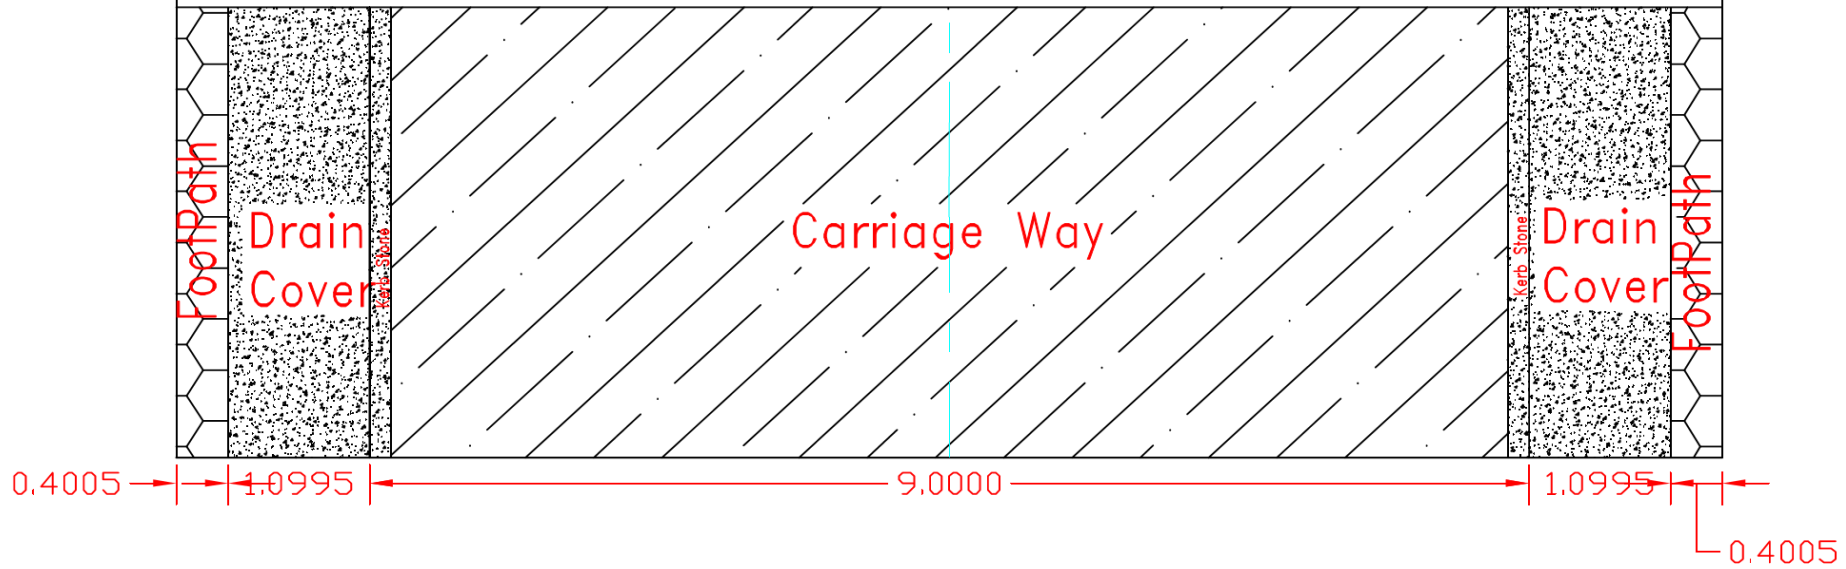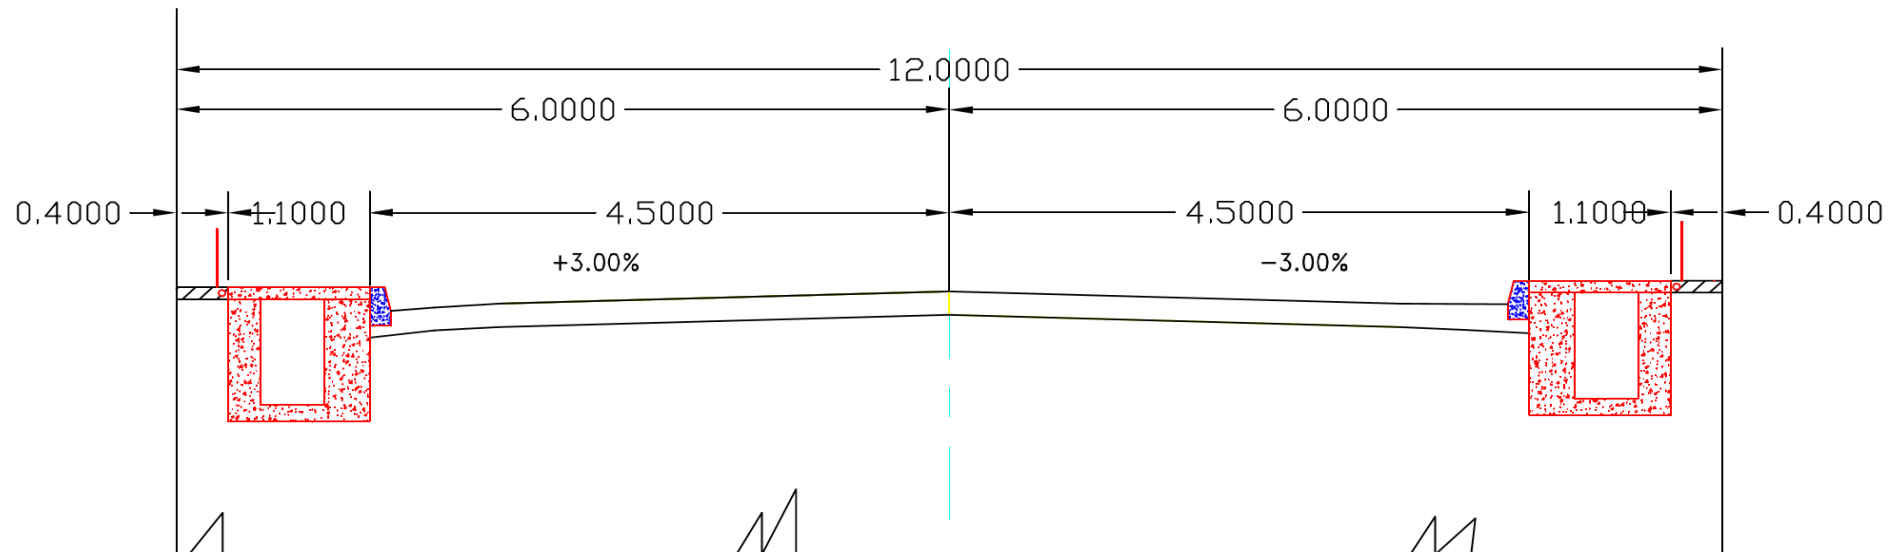

Gallamandi Road

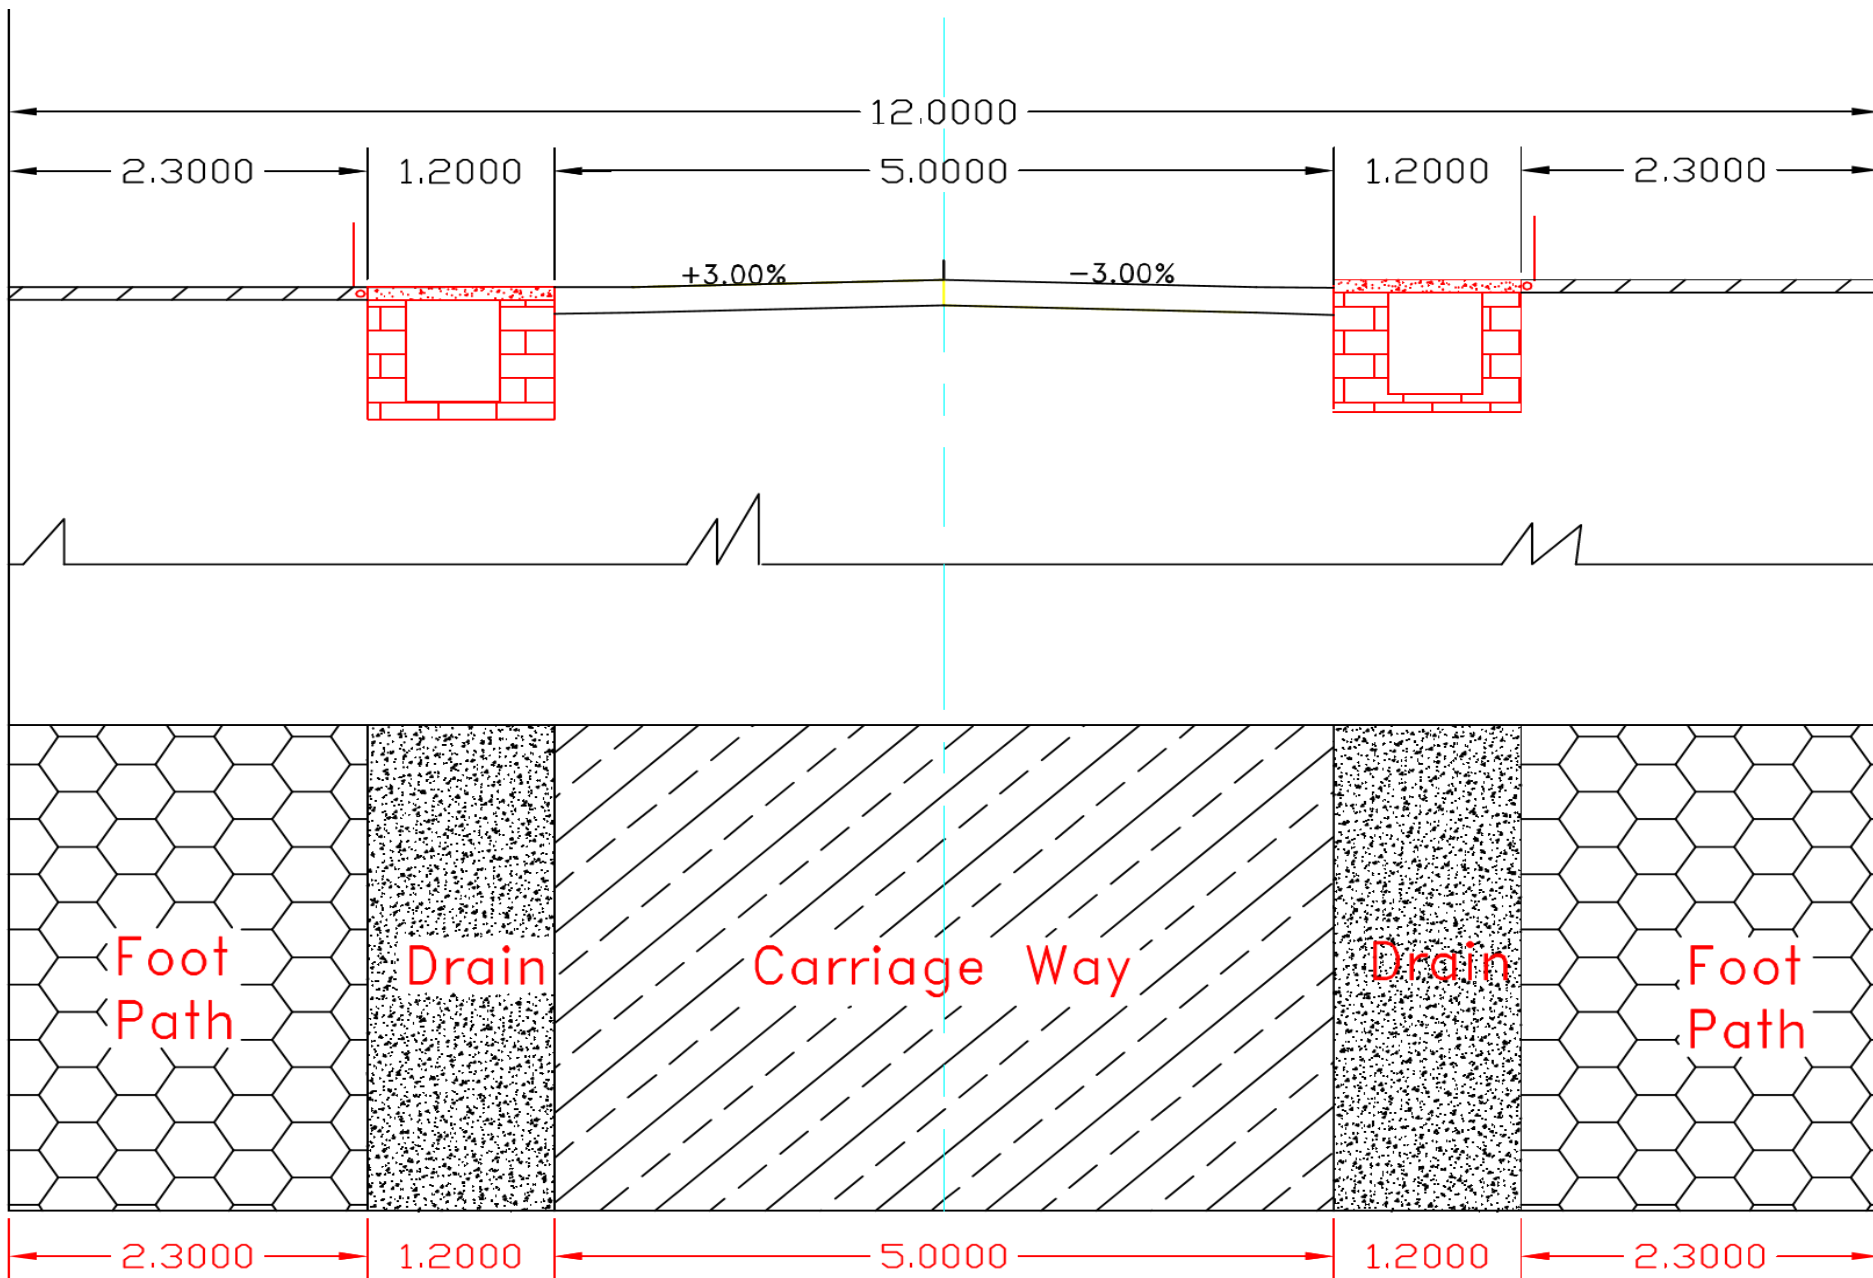


Khajana Path




# EIA / IEE Progress

Description	Progress Status
EIA for ISWM sub project	<ol style="list-style-type: none"><li>1. TOR and Scoping has been approved.</li><li>2. Public hearing has been conducted in proposed site and some issues has been raised by the local people.</li><li>3. Draft report has been submitted for comment. <b>DSC is preparing final report.</b></li></ol>
IEE for road and drain sub project	<ol style="list-style-type: none"><li>1. Final report has been submitted .</li><li>2. Presentation of final report has been done.</li><li>3. Final report incorporating comments has been submitted for approval. <b>Final report has been send to MoUD.</b></li></ol>

## Progress as time

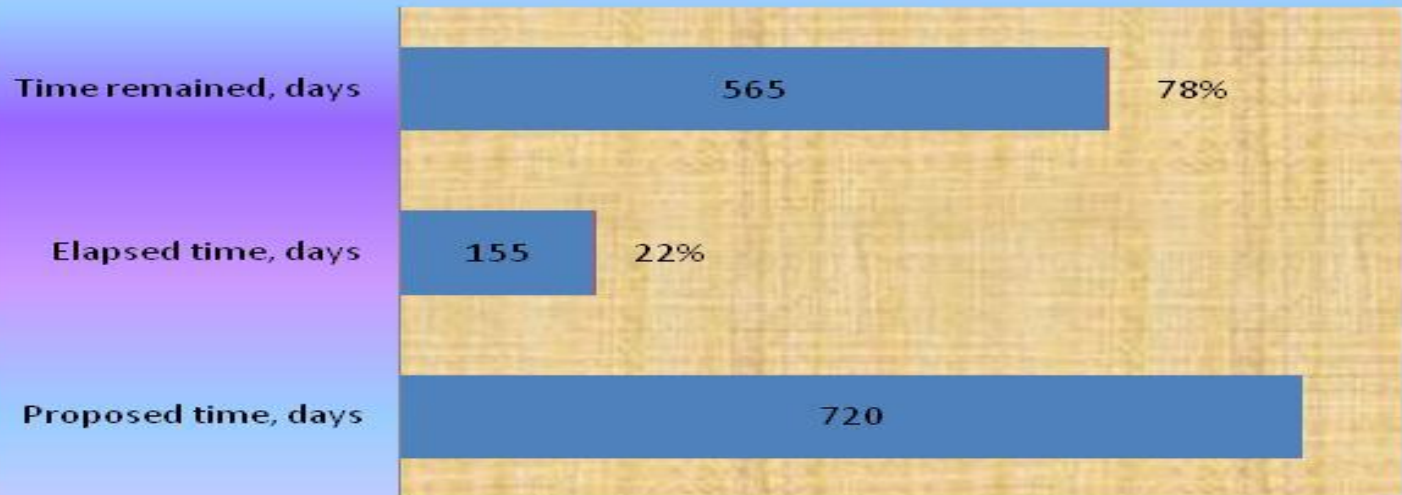

## Progress as value

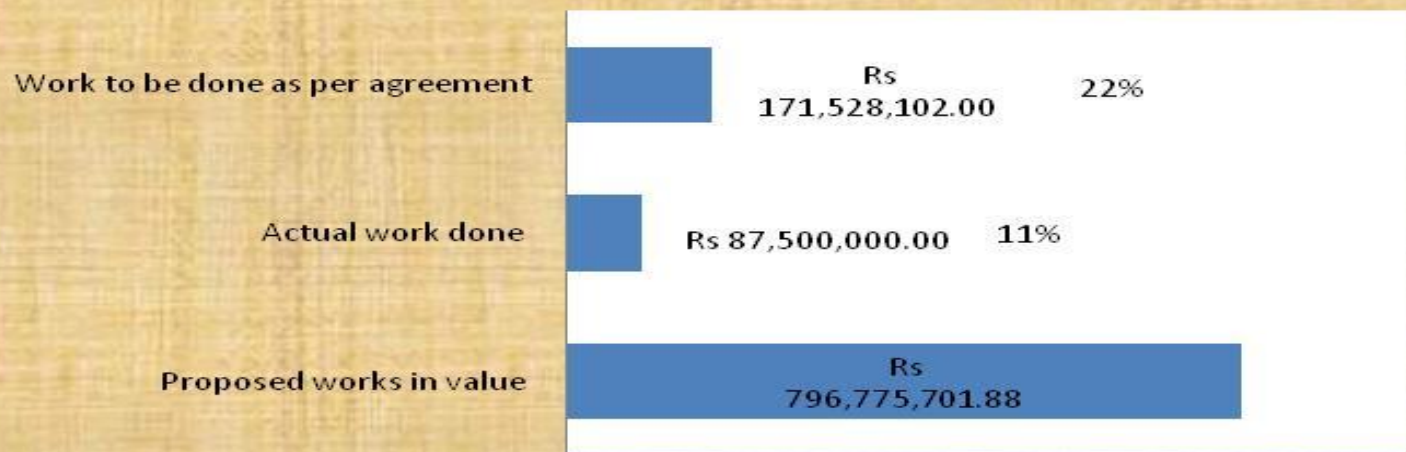

# Construction of drain and inspection by Municipality / PCO / PMSC



## Construction of drain



## Construction of drain, Gabion work and cover slab



## Construction of drain and drain cleaning by ditch cleaner



# Program Conducted by NGO

- Completed the upgrading of drain and Road in Gonahiya under the pilot project.
- 5 days street cleaning campaign within municipality core city and in all 13 wards.
- Completed four skill development training for the poor in poverty clusters. (Light vehicle driving – 48 persons, House wiring – 25 persons, Plumbing – 19 persons and Computer Hardware – 25 persons) training from 6 Chaitra 2071 to Aashad 2072.
- Solid waste management orientation class in all 13 wards and formed ward level solid waste management and sanitation committee.

# Program Conducted by NGO

- Wall painting in Municipality area with the awareness message of solid waste management, health, hygiene and sanitation.
- Hand-washing and tooth brushing demonstration in 2 school n 1 poverty cluster.
- FM/Radio broadcasting with the message of public awareness.
- One day “kitchen composting training” for all the TLO’s members of 20 poverty clusters.
- Use of bin demonstration in 5 places of core area of municipality with the message of solid waste management.



# Program Conducted by NGO

- Secondary school level speech competition between 6 school with the perspective of capacity building.
- 2 days “account keeping training” for the key persons of TLO’s members.
- Agreement between PIU and five User’s Group Committee for the construction of small scale community infrastructure.

# Awareness on health and hygiene in community





**NGO Public health expert Mr. Satrughna Ojha is discussing awareness of health and hygiene in Bhujauli poverty cluster**



**NGO Public health expert Mr. Satrughna Ojha is discussing awareness of health and hygiene in Chamartole poverty cluster**

# Wall painting for the public awareness with the message of health and hygiene

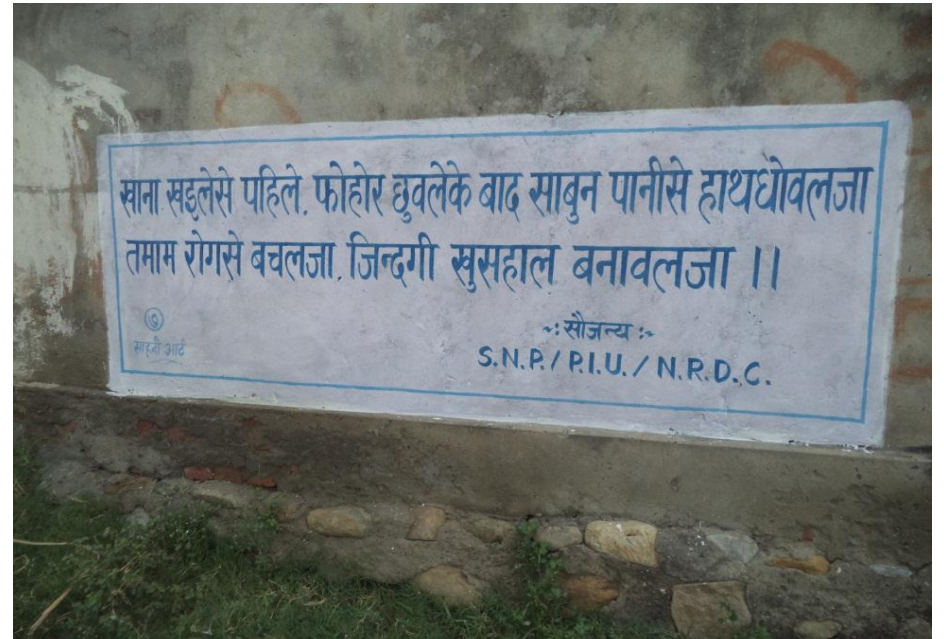

# Drain construction work of Pilot Project at Raghunathpur, Ward No. 9



# Opening Ceremony of Skill Training



**Welcome speech for skill training participants by CDO Mr. Toyam Rayamajhi**



**Welcome speech for skill training participants by Executive Officer Mr. Bishnu Datta Gautam**

# Ward Cleaning Campaign



**Executive Officer is participating in street cleaning campaign**



**Cleaning the drain by local people**

# Skills and Entrepreneurship Development Training



**Light Vehicle Driving Training Participants**



**Junior Computer Hardware Training Participants**

# Skills and Entrepreneurship Development Training



**House wiring Training participants**



**Plumbing Training Participants**



# Health and hygiene training



# Kitchen composting training



# Demonstration of use of bin



# Primary school level sports competition



# Secondary School level speech competition



# Hand washing and tooth brushing demonstration



# Financial Activity as of Ashadh 2072

## Incremental Recurrent income / expenditure

Source	Fund Received	Expenditure	Balance
GoN	1,674,000.00	1,102,957.02	571,042.98
ADB	4,526,000.00	2,960,568.84	1,565,431.16
TDF	0.00	0.00	0.00
Siddharthanagar Municipality	1,741,511.09	1,741,511.09	0.00
Others (Interest Income etc.)	0.00	0.00	0.00
<b>Total :</b>	<b>7,941,511.09</b>	<b>5,805,036.95</b>	<b>2,136,474.14</b>

# Financial Activity as of Ashadh 2072

## Capital Income/Expenditure

Source	Fund Received	Expenditure	Balance
GoN	45,472,049.00	41,113,038.29	<b>4,359,010.71</b>
ADB	106,322,522.45	101,068,409.15	5,254,113.30
TDF	15,189,653.00	15,189,653.00	0.00
Municipality	7,241,617.30	7,241,617.30	0.00
<b>Total</b>	<b>174,225,841.75</b>	<b>164,612,717.74</b>	<b>9,613,124.01</b>



# Financial Activity as of Ashadh 2072

## Total Income/Expenditure

Source	Fund Received	Expenditure	Balance
<b>Total Incremental Recurrent :</b>	7,941,511.09	5,805,036.95 <b>(73%)</b>	2,136,474.14
<b>Total of Capital Income/Expenditure:</b>	174,225,841.75	164,612,717.74 <b>(95%)</b>	9,613,124.01
<b>Total :</b>	<b>182,167,352.84</b>	<b>170,417,754.69</b> <b>(94%)</b>	<b>11,749,598.15</b>

# Total Financial Activity

## Total Income/Expenditure

Source	Fund Received	Expenditure	Balance
Total of F.Y.2069/70	17,400,000.00	17,396,832.27	3,167.73
Total of F.Y.2070/71	44,082,144.74	44,082,144.74	0.00
Total of F.Y.2071/72	182,167,352.84	170,417,754.69	11,749,598.15
<b>Total :</b>	<b>243,649,497.58</b>	<b>231,896,731.70</b>	<b>11,752,765.88</b>

# Issues

Existing water supply line is running in the center line of the road which are to be relocate. Similarly there was no provision of foot path and sufficient budget for relocation of electric and telephone poles but ADB has allocated additional fund for these utilities. So we are grateful to ADB.

Right of way of road is insufficient to locate all the utilities in some roads. We are unable to increase the right of way of roads since compensation for the land and building is not allocated in budget. Those buildings were constructed before the right of way was implemented by the Municipal Council.

# अतिरिक्त लगानी (Additional Financing) सम्बन्धमा

- Ad memoire (ADB mission को) अनुसार सिद्धार्थनगर नगरपालिकामा अतिरिक्त लगानी गर्ने सैद्धान्तिक सहमति भएको ।
- अतिरिक्त लगानीमा हाल निर्माणाधिन र प्रस्तावित सडकहरुमा फुटपाथ, ग्रीनरी बनाउन प्रस्ताव गरिएको ।
- सडकको दुवै तर्फ खानेपानी, टेलिफोन र बिजुलीको लाईन विस्तार प्रस्ताव गरिएको ।
- अतिरिक्त कालोपत्रे थप २३ कि.मी. (सडकको दुवै तर्फ सतह ड्रेन समेत) प्रस्ताव गरिएको ।

# THANK YOU!!!

